


PROJECT SCHEDULE (GANTT CHART)

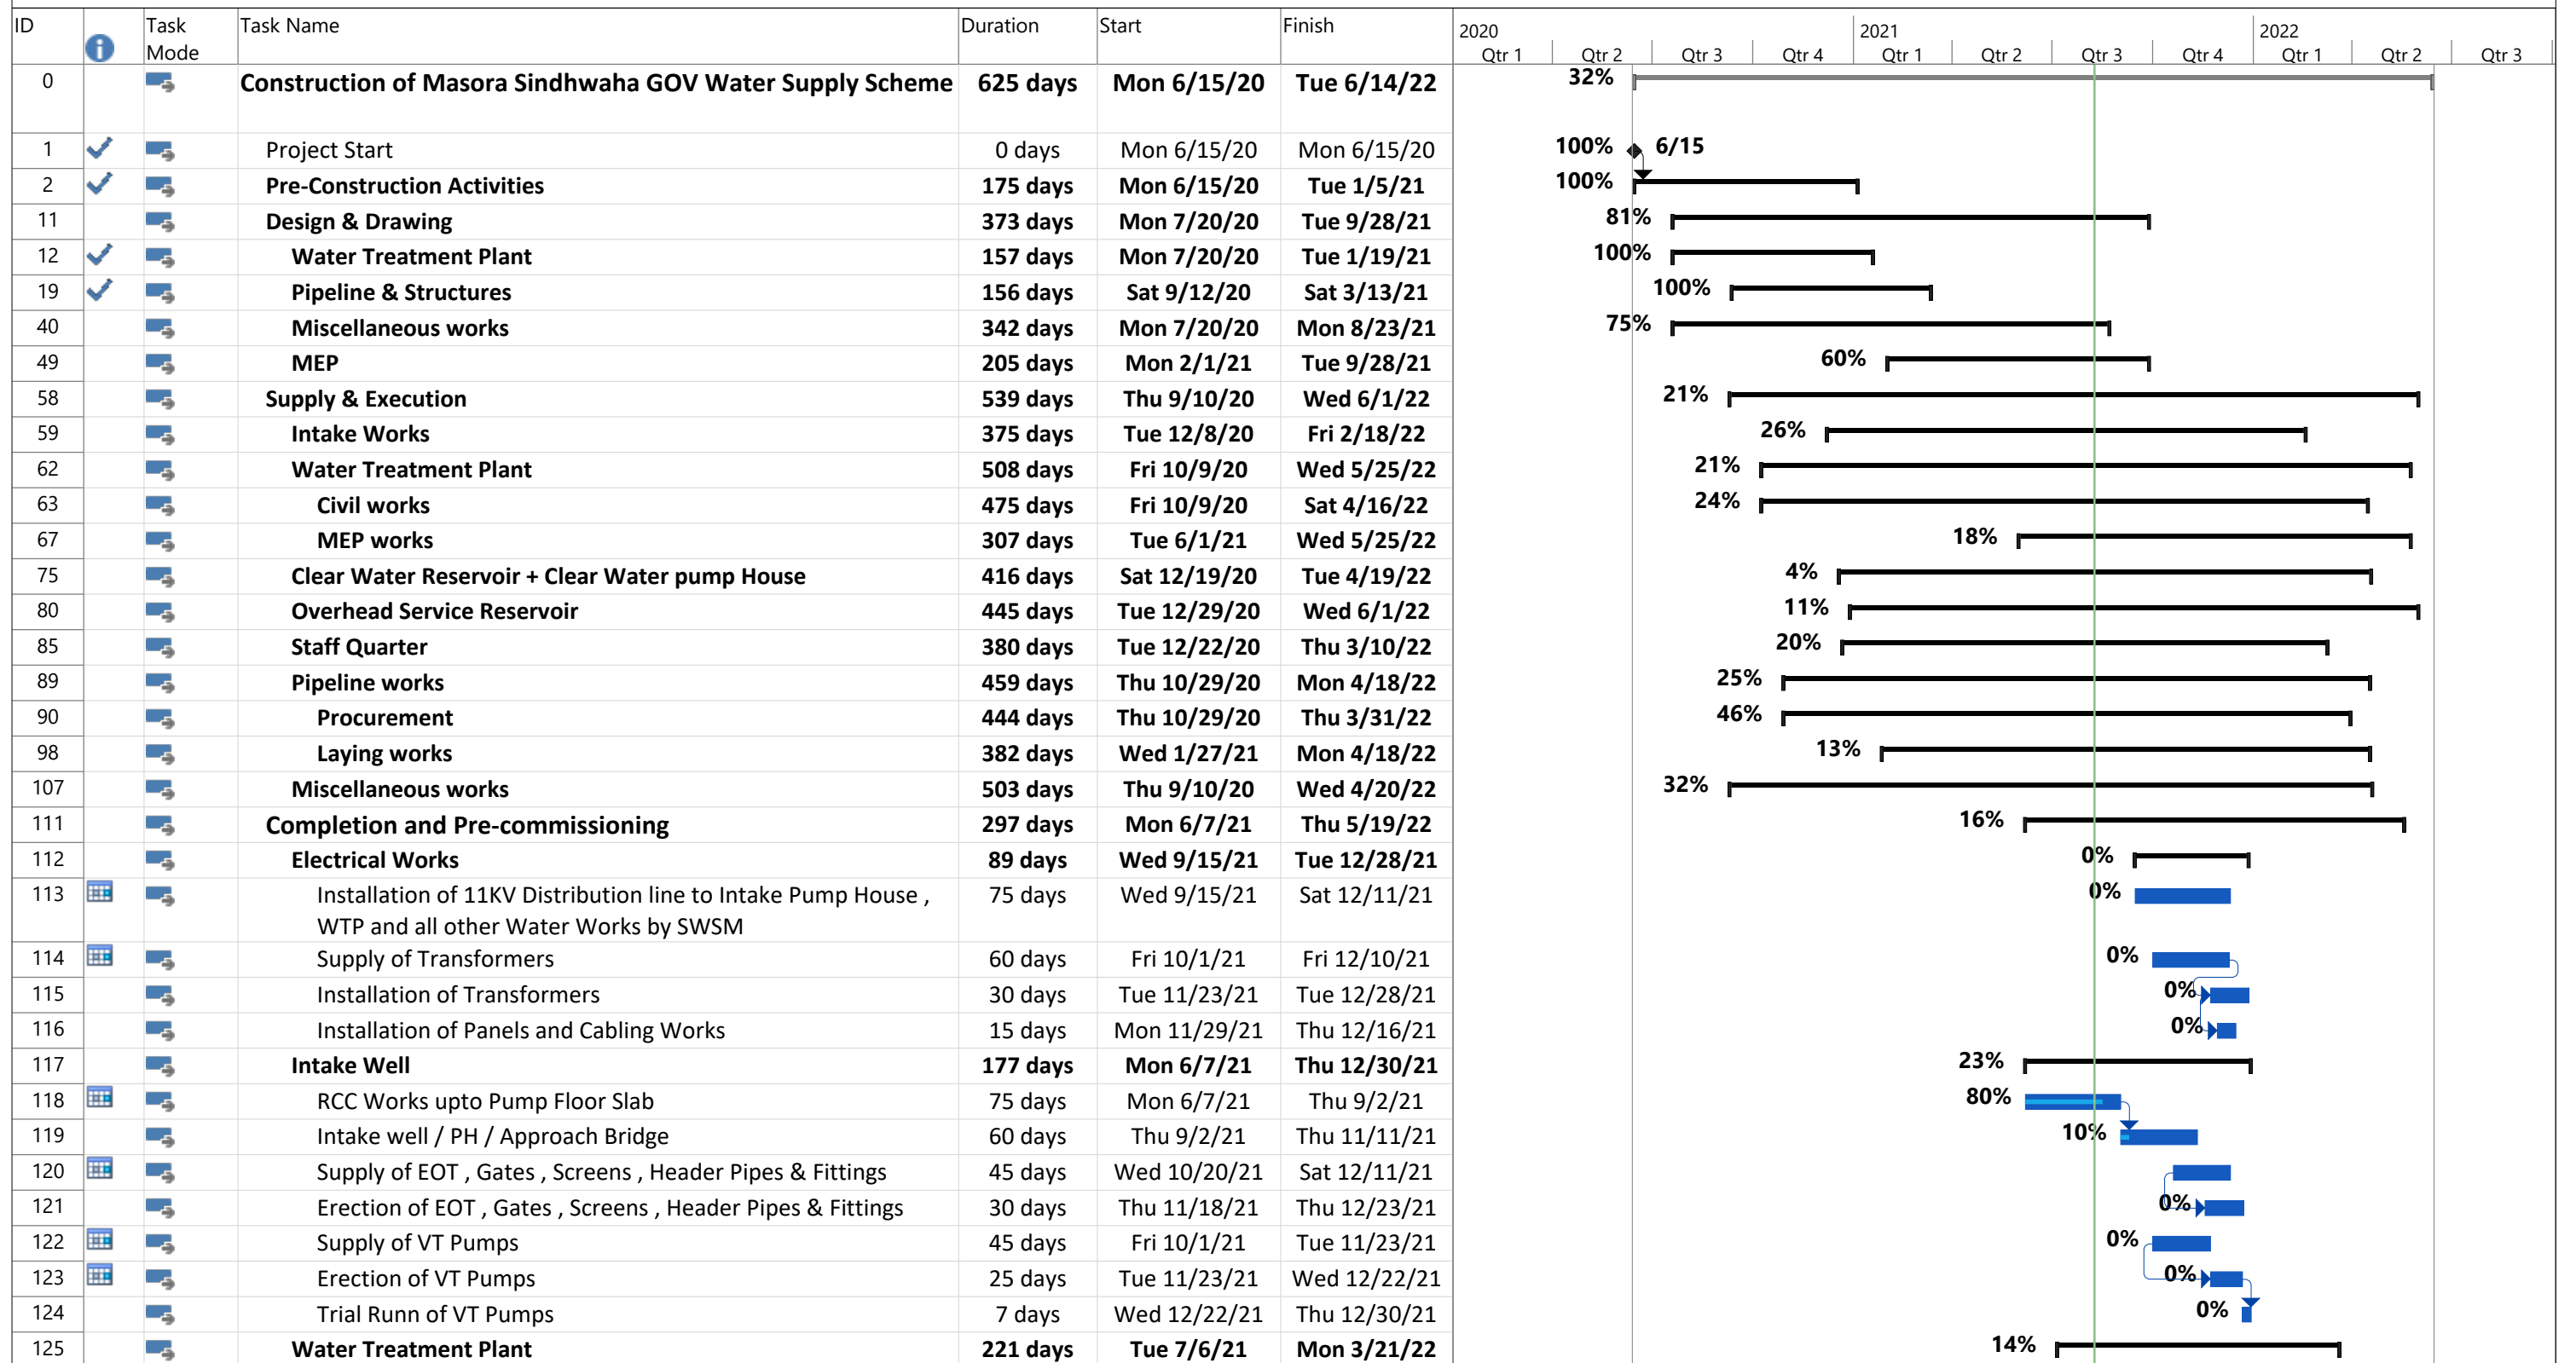

PERT CHART

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

PROJECT SCHEDULE (GANTT CHART)

ID	Task Mode	Task Name	Duration	Start	Finish	2020				2021				2022		
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
126		Completion of Civil Works	180 days	Tue 7/6/21	Tue 2/1/22									25%		
127		Procurement of WTP Equipments	75 days	Mon 11/1/21	Thu 1/27/22									0%		
128		Erection of WTP Equipments	30 days	Wed 2/2/22	Wed 3/9/22									0%		
129		Electrical Cabling Works	30 days	Wed 2/2/22	Wed 3/9/22									0%		
130		Trial Run of WTP	10 days	Wed 3/9/22	Mon 3/21/22									0%		
131		Zone -1 (Sindhwaha) ,Zone - 3(Bejinath),Zone -7(Silawan), Zone -11(Khjuriya),Zone -12(Khitwans)	150 days	Tue 7/6/21	Tue 12/28/21									24%		
132		CWR Completion	101 days	Tue 7/6/21	Mon 11/1/21									6%		
133		Supply of VT Pumps , EOT , Header Pipes and Fittings	45 days	Fri 10/1/21	Tue 11/23/21									0%		
134		Erection of VT Pumps , EOT , Header Pipes and Fittings	25 days	Tue 11/23/21	Wed 12/22/21									0%		
135		OHT Completion	120 days	Tue 7/6/21	Tue 11/23/21									35%		
136		Installation of inlate/ Outlate (DI/DF) Pipes and valves	15 days	Tue 11/23/21	Fri 12/10/21									0%		
137		Rising Main Works	75 days	Wed 9/1/21	Sat 11/27/21									56%		
138		Distribution Main Works	125 days	Tue 7/6/21	Mon 11/29/21									39%		
139		House Service Connections	75 days	Fri 10/1/21	Tue 12/28/21									0%		
140		Other Zone	272 days	Tue 7/6/21	Thu 5/19/22									0%		
141		CWR Completion	210 days	Tue 7/6/21	Tue 3/8/22									0%		
142		Supply of VT Pumps , EOT , Header Pipes and Fittings	60 days	Sat 1/1/22	Sat 3/12/22									13%		
143		Erection of VT Pumps , EOT , Header Pipes and Fittings	30 days	Sat 3/12/22	Sat 4/16/22									0%		
144		OHT Completion	210 days	Tue 7/6/21	Tue 3/8/22									30%		
145		Installation of inlate/ Outlate (DI/DF) Pipes and valves	25 days	Tue 3/8/22	Wed 4/6/22									6%		
146		Rising Main Works	210 days	Tue 7/6/21	Tue 3/8/22									25%		
147		Distribution Main Works	250 days	Tue 7/6/21	Sat 4/23/22									0%		
148		House Service Connections	122 days	Tue 12/28/21	Thu 5/19/22									0%		
149		Trial Run and Commissioning of Entire Scheme	22 days	Thu 5/19/22	Tue 6/14/22									0%		
150		Trial run of system	15 days	Thu 5/19/22	Mon 6/6/22									0%		
151		Final Commissioning of system	7 days	Mon 6/6/22	Tue 6/14/22									0%		

PERT CHART

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
