


Project: Jhilo Construction Schedule Date: 06-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

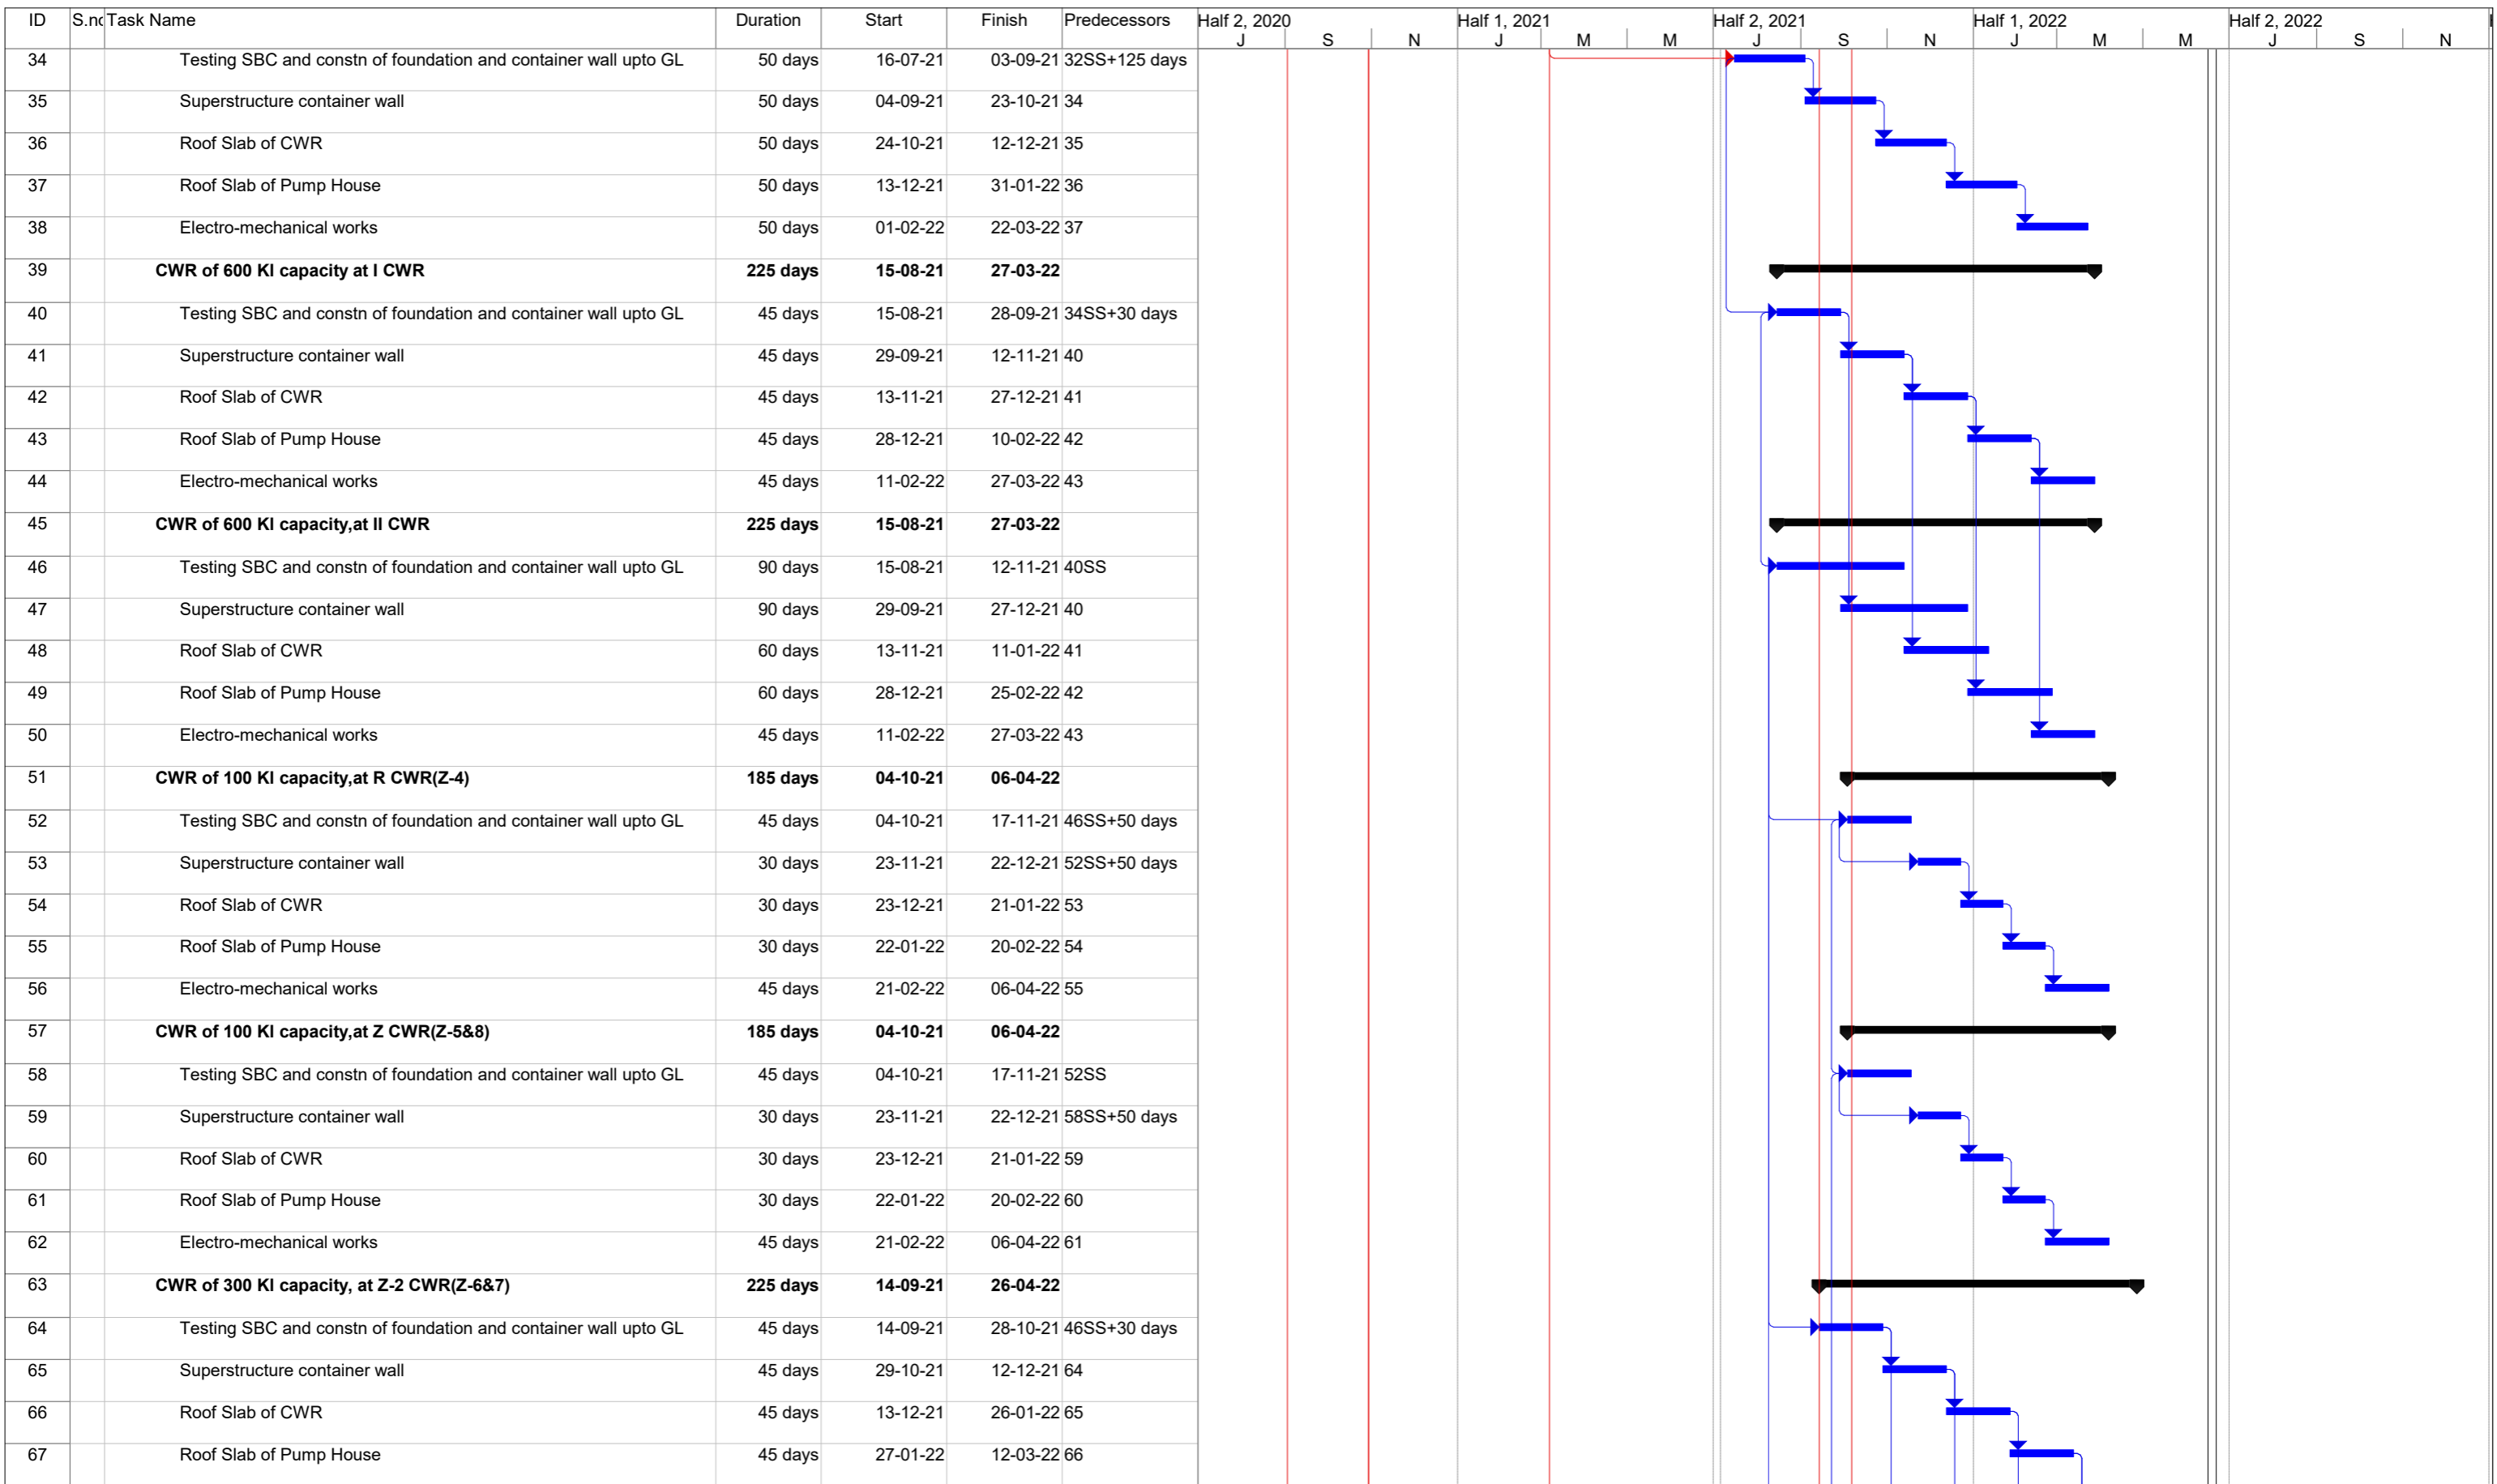


Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
68		Electro-mechanical works	45 days	13-03-22	26-04-22	67																
69		CWR of 50 KI capacity, at Z-1 CWR(Z-9&10)	150 days	26-07-21	22-12-21																	
70		Testing SBC and constn of foundation and container wall upto GL	30 days	26-07-21	24-08-21	32SS+135 days																
71		Superstructure container wall	30 days	25-08-21	23-09-21	70SS+30 days																
72		Roof Slab of CWR	30 days	24-09-21	23-10-21	71																
73		Roof Slab of Pump House	30 days	24-10-21	22-11-21	72																
74		Electro-mechanical works	30 days	23-11-21	22-12-21	73																
75		CWR of 100 KI capacity, at Z-1 CWR(Z-9&10)	185 days	04-10-21	06-04-22																	
76		Testing SBC and constn of foundation and container wall upto GL	45 days	04-10-21	17-11-21	58SS																
77		Superstructure container wall	30 days	23-11-21	22-12-21	76SS+50 days																
78		Roof Slab of CWR	30 days	23-12-21	21-01-22	77																
79		Roof Slab of Pump House	30 days	22-01-22	20-02-22	78																
80		Electro-mechanical works	45 days	21-02-22	06-04-22	79																
81		CWR of 200 KI capacity, at Z-1 CWR(Z-9&10)	225 days	14-09-21	26-04-22																	
82		Testing SBC and constn of foundation and container wall upto GL	45 days	14-09-21	28-10-21	46SS+30 days																
83		Superstructure container wall	45 days	29-10-21	12-12-21	64																
84		Roof Slab of CWR	45 days	13-12-21	26-01-22	65																
85		Roof Slab of Pump House	45 days	27-01-22	12-03-22	66																
86		Electro-mechanical works	45 days	13-03-22	26-04-22	67																
87		CWR of 100 KI capacity, at Z-1 CWR(Z-9&10)	180 days	02-11-21	30-04-22																	
88		Testing SBC and constn of foundation and container wall upto GL	45 days	02-11-21	16-12-21	76SS+29 days																
89		Superstructure container wall	30 days	17-12-21	15-01-22	88																
90		Roof Slab of CWR	30 days	16-01-22	14-02-22	89																
91		Roof Slab of Pump House	30 days	15-02-22	16-03-22	90																
92		Electro-mechanical works	45 days	17-03-22	30-04-22	91																
93		CWR of 100 KI capacity, at Z-1 CWR(Z-9&10)	180 days	02-11-21	30-04-22																	
94		Testing SBC and constn of foundation and container wall upto GL	45 days	02-11-21	16-12-21	76SS+29 days																
95		Superstructure container wall	30 days	17-12-21	15-01-22	88																
96		Roof Slab of CWR	30 days	16-01-22	14-02-22	89																
97		Roof Slab of Pump House	30 days	15-02-22	16-03-22	90																
98		Electro-mechanical works	45 days	17-03-22	30-04-22	91																
99		CWR of 50 KI capacity, at Z-1 CWR(Z-9&10)	150 days	02-12-21	30-04-22																	
100		Testing SBC and constn of foundation and container wall upto GL	30 days	02-12-21	31-12-21	94SS+30 days																
101		Superstructure container wall	30 days	01-01-22	30-01-22	100																

Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

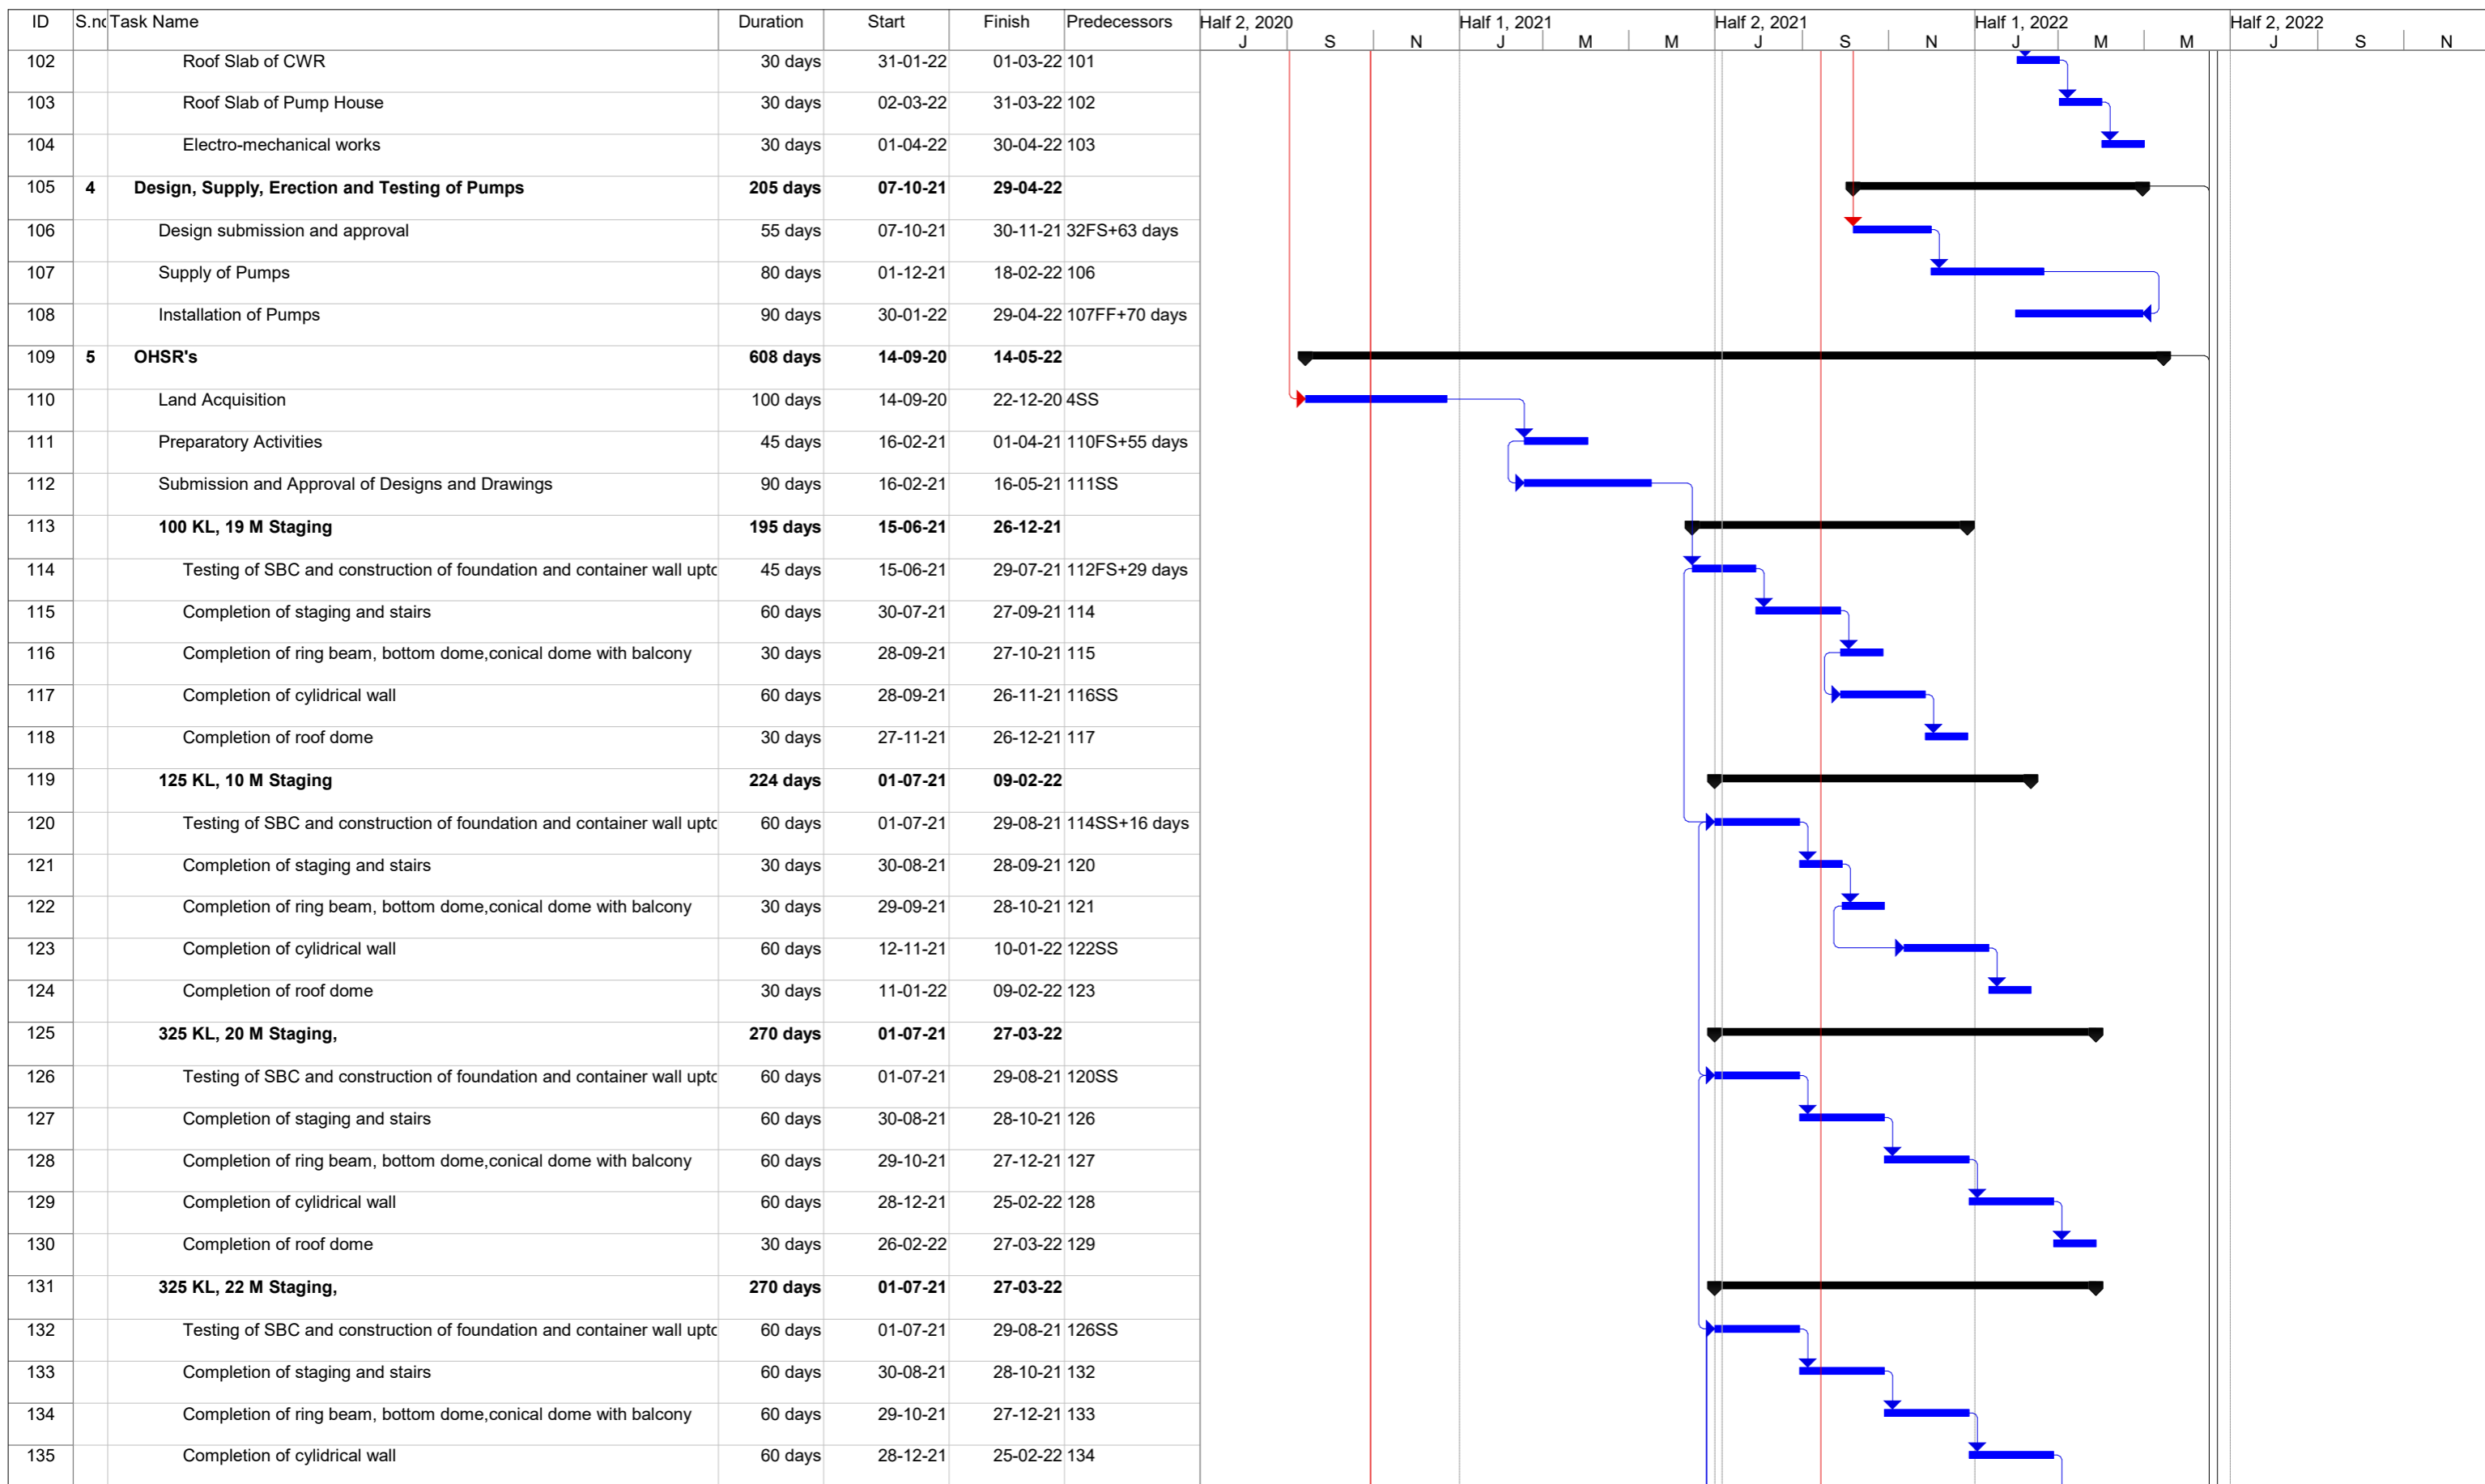

Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			


ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
136		Completion of roof dome	30 days	26-02-22	27-03-22	135																
137		275 KL, 8 M Staging,	240 days	15-08-21	11-04-22																	
138		Testing of SBC and construction of foundation and container wall upto	60 days	15-08-21	13-10-21	132SS+45 days																
139		Completion of staging and stairs	60 days	14-10-21	12-12-21	138																
140		Completion of ring beam, bottom dome, conical dome with balcony	45 days	13-12-21	26-01-22	139																
141		Completion of cylindrical wall	45 days	27-01-22	12-03-22	140																
142		Completion of roof dome	30 days	13-03-22	11-04-22	141																
143		150 KL, 13 M Staging,	210 days	02-09-21	30-03-22																	
144		Testing of SBC and construction of foundation and container wall upto	60 days	02-09-21	31-10-21	138SS+18 days																
145		Completion of staging and stairs	30 days	01-11-21	30-11-21	144																
146		Completion of ring beam, bottom dome, conical dome with balcony	30 days	01-12-21	30-12-21	145																
147		Completion of cylindrical wall	60 days	31-12-21	28-02-22	146																
148		Completion of roof dome	30 days	01-03-22	30-03-22	147																
149		175 KL, 22 M Staging, at Matna.	210 days	21-07-21	15-02-22																	
150		Testing of SBC and construction of foundation and container wall upto	60 days	21-07-21	18-09-21	132SS+20 days																
151		Completion of staging and stairs	30 days	19-09-21	18-10-21	150																
152		Completion of ring beam, bottom dome, conical dome with balcony	30 days	19-10-21	17-11-21	151																
153		Completion of cylindrical wall	60 days	18-11-21	16-01-22	152																
154		Completion of roof dome	30 days	17-01-22	15-02-22	153																
155		175 KL, 8 M Staging, at Matna.	210 days	02-09-21	30-03-22																	
156		Testing of SBC and construction of foundation and container wall upto	60 days	02-09-21	31-10-21	144SS																
157		Completion of staging and stairs	30 days	01-11-21	30-11-21	156																
158		Completion of ring beam, bottom dome, conical dome with balcony	30 days	01-12-21	30-12-21	157																
159		Completion of cylindrical wall	60 days	31-12-21	28-02-22	158																
160		Completion of roof dome	30 days	01-03-22	30-03-22	159																
161		25 KL, 8 M Staging	150 days	01-12-21	29-04-22																	
162		Testing of SBC and construction of foundation and container wall upto	30 days	01-12-21	30-12-21	156SS+90 days																
163		Completion of staging and stairs	30 days	31-12-21	29-01-22	162																
164		Completion of ring beam, bottom dome, conical dome with balcony	30 days	30-01-22	28-02-22	163																
165		Completion of cylindrical wall	30 days	01-03-22	30-03-22	164																
166		Completion of roof dome	30 days	31-03-22	29-04-22	165																
167		200 KL, 19 M Staging	225 days	15-08-21	27-03-22																	
168		Testing of SBC and construction of foundation and container wall upto	30 days	15-08-21	13-09-21	138SS																
169		Completion of staging and stairs	60 days	14-09-21	12-11-21	168																

Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022					
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N			
170		Completion of ring beam, bottom dome, conical dome with balcony	45 days	13-11-21	27-12-21	169																		
171		Completion of cylindrical wall	60 days	28-12-21	25-02-22	170																		
172		Completion of roof dome	30 days	26-02-22	27-03-22	171																		
173		25 KL, 8 M Staging	150 days	01-12-21	29-04-22																			
174		Testing of SBC and construction of foundation and container wall upto	30 days	01-12-21	30-12-21	162SS																		
175		Completion of staging and stairs	30 days	31-12-21	29-01-22	174																		
176		Completion of ring beam, bottom dome, conical dome with balcony	30 days	30-01-22	28-02-22	175																		
177		Completion of cylindrical wall	30 days	01-03-22	30-03-22	176																		
178		Completion of roof dome	30 days	31-03-22	29-04-22	177																		
179		100 KL, 8 M Staging	195 days	04-10-21	16-04-22																			
180		Testing of SBC and construction of foundation and container wall upto	45 days	04-10-21	17-11-21	168SS+50 days																		
181		Completion of staging and stairs	60 days	18-11-21	16-01-22	180																		
182		Completion of ring beam, bottom dome, conical dome with balcony	30 days	17-01-22	15-02-22	181																		
183		Completion of cylindrical wall	60 days	17-01-22	17-03-22	182SS																		
184		Completion of roof dome	30 days	18-03-22	16-04-22	183																		
185		175 KL, 12 M Staging	210 days	15-08-21	12-03-22																			
186		Testing of SBC and construction of foundation and container wall upto	60 days	15-08-21	13-10-21	168SS																		
187		Completion of staging and stairs	30 days	14-10-21	12-11-21	186																		
188		Completion of ring beam, bottom dome, conical dome with balcony	30 days	13-11-21	12-12-21	187																		
189		Completion of cylindrical wall	60 days	13-12-21	10-02-22	188																		
190		Completion of roof dome	30 days	11-02-22	12-03-22	189																		
191		150 KL, 15 M Staging	210 days	15-08-21	12-03-22																			
192		Testing of SBC and construction of foundation and container wall upto	60 days	15-08-21	13-10-21	186SS																		
193		Completion of staging and stairs	30 days	14-10-21	12-11-21	192																		
194		Completion of ring beam, bottom dome, conical dome with balcony	30 days	13-11-21	12-12-21	193																		
195		Completion of cylindrical wall	60 days	13-12-21	10-02-22	194																		
196		Completion of roof dome	30 days	11-02-22	12-03-22	195																		
197		175 KL, 20 M Staging	210 days	25-08-21	22-03-22																			
198		Testing of SBC and construction of foundation and container wall upto	60 days	25-08-21	23-10-21	192SS+10 days																		
199		Completion of staging and stairs	30 days	24-10-21	22-11-21	198																		
200		Completion of ring beam, bottom dome, conical dome with balcony	30 days	23-11-21	22-12-21	199																		
201		Completion of cylindrical wall	60 days	23-12-21	20-02-22	200																		
202		Completion of roof dome	30 days	21-02-22	22-03-22	201																		
203		125 KL, 8 M Staging	195 days	01-11-21	14-05-22																			

Project: Jhilo Construction Schedule Date: 06-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

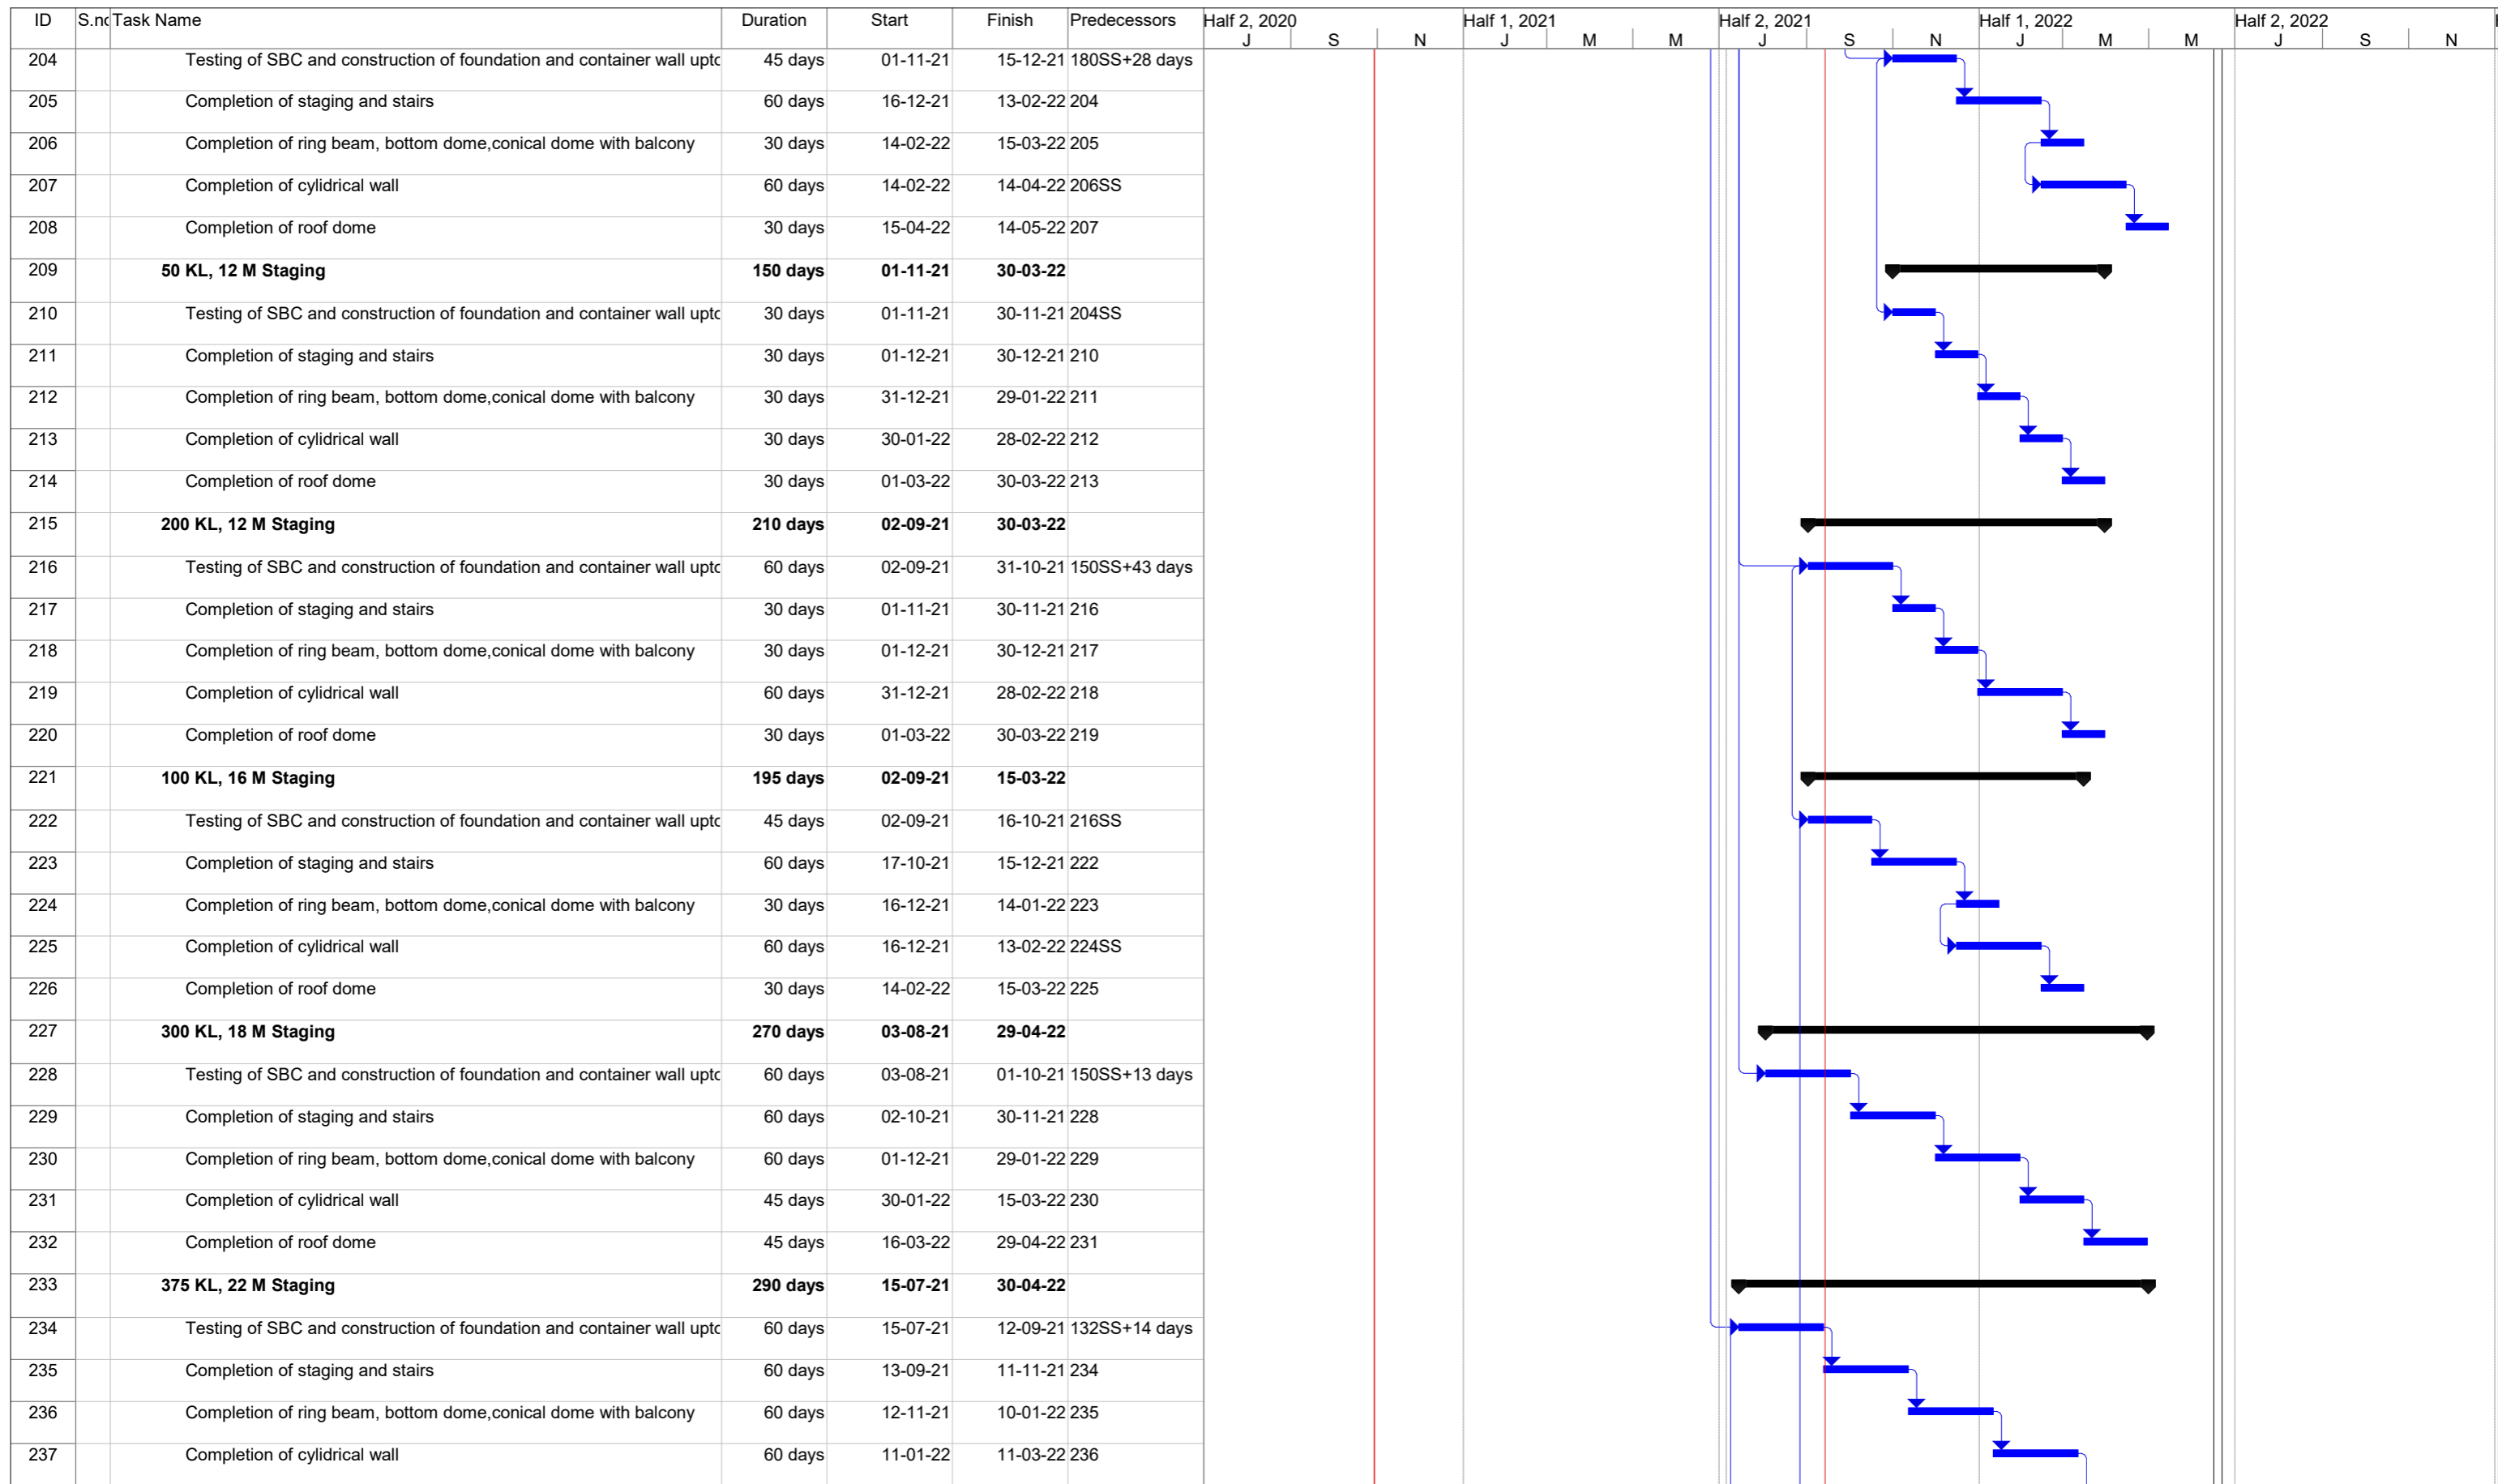


Project: Jhilo Construction Schedule Date: 06-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
238		Completion of roof dome	50 days	12-03-22	30-04-22	237																
239		75 KL, 22 M Staging	150 days	02-10-21	28-02-22																	
240		Testing of SBC and construction of foundation and container wall upto	30 days	02-10-21	31-10-21	222SS+30 days																
241		Completion of staging and stairs	30 days	01-11-21	30-11-21	240																
242		Completion of ring beam, bottom dome, conical dome with balcony	30 days	01-12-21	30-12-21	241																
243		Completion of cylindrical wall	30 days	31-12-21	29-01-22	242																
244		Completion of roof dome	30 days	30-01-22	28-02-22	243																
245		100 KL, 8 M Staging	195 days	01-11-21	14-05-22																	
246		Testing of SBC and construction of foundation and container wall upto	45 days	01-11-21	15-12-21	240SS+30 days																
247		Completion of staging and stairs	45 days	16-12-21	29-01-22	246																
248		Completion of ring beam, bottom dome, conical dome with balcony	45 days	30-01-22	15-03-22	247																
249		Completion of cylindrical wall	30 days	16-03-22	14-04-22	248																
250		Completion of roof dome	30 days	15-04-22	14-05-22	249																
251		175 KL, 15 M Staging	225 days	14-08-21	26-03-22																	
252		Testing of SBC and construction of foundation and container wall upto	45 days	14-08-21	27-09-21	234SS+30 days																
253		Completion of staging and stairs	60 days	28-09-21	26-11-21	252																
254		Completion of ring beam, bottom dome, conical dome with balcony	45 days	27-11-21	10-01-22	253																
255		Completion of cylindrical wall	45 days	11-01-22	24-02-22	254																
256		Completion of roof dome	30 days	25-02-22	26-03-22	255																
257		275 KL, 22 M Staging	240 days	14-08-21	10-04-22																	
258		Testing of SBC and construction of foundation and container wall upto	45 days	14-08-21	27-09-21	252SS																
259		Completion of staging and stairs	60 days	28-09-21	26-11-21	258																
260		Completion of ring beam, bottom dome, conical dome with balcony	60 days	27-11-21	25-01-22	259																
261		Completion of cylindrical wall	45 days	26-01-22	11-03-22	260																
262		Completion of roof dome	30 days	12-03-22	10-04-22	261																
263		100 KL, 16 M Staging	195 days	03-09-21	16-03-22																	
264		Testing of SBC and construction of foundation and container wall upto	45 days	03-09-21	17-10-21	258SS+20 days																
265		Completion of staging and stairs	45 days	18-10-21	01-12-21	264																
266		Completion of ring beam, bottom dome, conical dome with balcony	45 days	02-12-21	15-01-22	265																
267		Completion of cylindrical wall	30 days	16-01-22	14-02-22	266																
268		Completion of roof dome	30 days	15-02-22	16-03-22	267																
269	7	Pipeline works	538 days	20-12-20	10-06-22																	
270		Submission and Approval of Hydraulic Designs and Drawings	170 days	20-12-20	07-06-21	7SS+45 days																
271		Pipe Delivery at Site after inspection	280 days	08-06-21	14-03-22	270																

Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

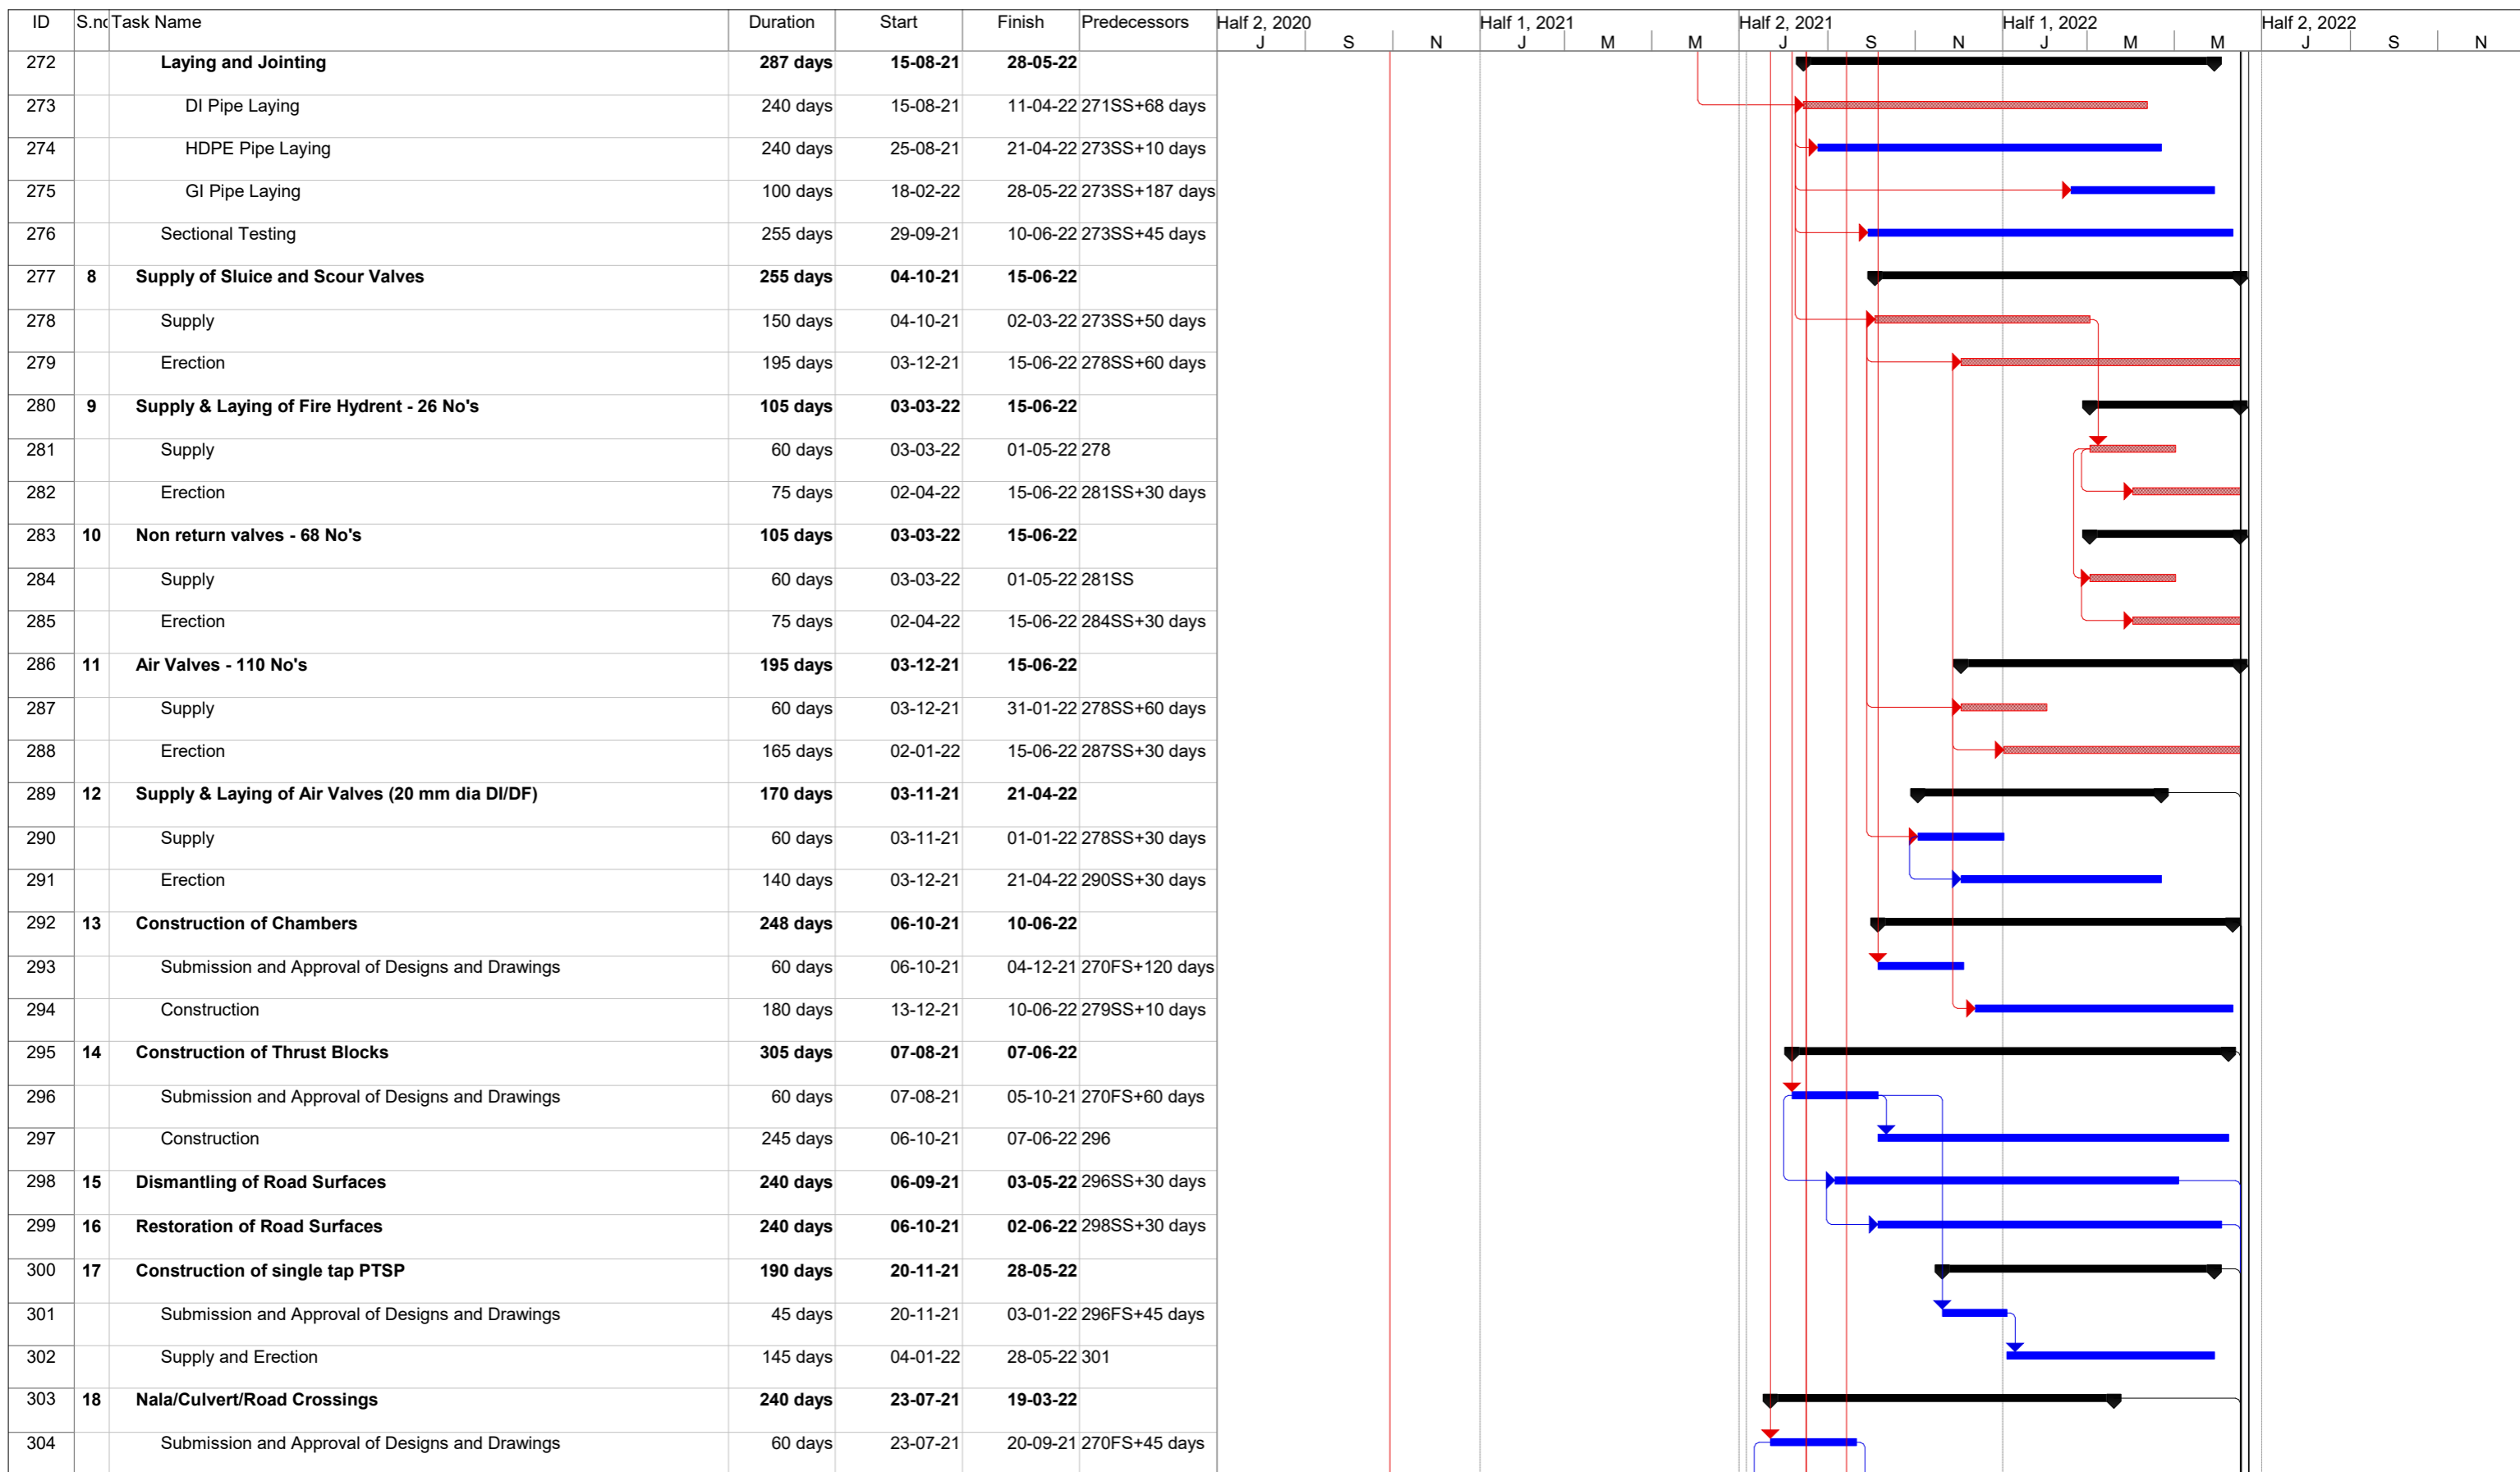

Project: Jhilo Construction Schedule
Date: 06-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

