


Project: Jhilo Construction Schedule Date: 07-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021		Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N
40		Testing SBC and constn of foundation and container wall upto GL	60 days	01-07-21	29-08-21	32SS+110 days															
41		Superstructure container wall	60 days	30-08-21	28-10-21	40															
42		Roof Slab of CWR	60 days	29-10-21	27-12-21	41															
43		Roof Slab of Pump House	45 days	28-12-21	10-02-22	42															
44		Electro-mechanical works	45 days	11-02-22	27-03-22	43															
45		CWR of 450 KI capacity at Bilrahi IPS	270 days	15-08-21	11-05-22																
46		Testing SBC and constn of foundation and container wall upto GL	60 days	15-08-21	13-10-21	40SS+45 days															
47		Superstructure container wall	60 days	14-10-21	12-12-21	46															
48		Roof Slab of CWR	60 days	13-12-21	10-02-22	47															
49		Roof Slab of Pump House	45 days	11-02-22	27-03-22	48															
50		Electro-mechanical works	45 days	28-03-22	11-05-22	49															
51		CWR of 275 KI capacity at Tolasoyam	230 days	04-10-21	21-05-22																
52		Testing SBC and constn of foundation and container wall upto GL	45 days	04-10-21	17-11-21	46SS+50 days															
53		Superstructure container wall	45 days	23-11-21	06-01-22	52SS+50 days															
54		Roof Slab of CWR	45 days	07-01-22	20-02-22	53															
55		Roof Slab of Pump House	45 days	21-02-22	06-04-22	54															
56		Electro-mechanical works	45 days	07-04-22	21-05-22	55															
57		CWR of 400 KI capacity at Mohan Pura/Indratha	245 days	04-10-21	05-06-22																
58		Testing SBC and constn of foundation and container wall upto GL	45 days	04-10-21	17-11-21	52SS															
59		Superstructure container wall	60 days	23-11-21	21-01-22	58SS+50 days															
60		Roof Slab of CWR	45 days	22-01-22	07-03-22	59															
61		Roof Slab of Pump House	45 days	08-03-22	21-04-22	60															
62		Electro-mechanical works	45 days	22-04-22	05-06-22	61															
63		CWR of 100 KI capacity at Sijwaha	165 days	14-09-21	25-02-22																
64		Testing SBC and constn of foundation and container wall upto GL	30 days	14-09-21	13-10-21	46SS+30 days															
65		Superstructure container wall	30 days	14-10-21	12-11-21	64															
66		Roof Slab of CWR	30 days	13-11-21	12-12-21	65															
67		Roof Slab of Pump House	30 days	13-12-21	11-01-22	66															
68		Electro-mechanical works	45 days	12-01-22	25-02-22	67															
69		CWR of 400 KI capacity at Tikariya Panwari	245 days	26-07-21	27-03-22																
70		Testing SBC and constn of foundation and container wall upto GL	45 days	26-07-21	08-09-21	32SS+135 days															
71		Superstructure container wall	60 days	14-09-21	12-11-21	70SS+50 days															
72		Roof Slab of CWR	45 days	13-11-21	27-12-21	71															
73		Roof Slab of Pump House	45 days	28-12-21	10-02-22	72															
74		Electro-mechanical works	45 days	11-02-22	27-03-22	73															
75		CWR of 650 KI capacity at Ajner IPS	275 days	25-08-21	26-05-22																
76		Testing SBC and constn of foundation and container wall upto GL	60 days	25-08-21	23-10-21	70SS+30 days															
77		Superstructure container wall	60 days	24-10-21	22-12-21	76															
78		Roof Slab of CWR	60 days	23-12-21	20-02-22	77															
79		Roof Slab of Pump House	50 days	21-02-22	11-04-22	78															

Project: Jhilo Construction Schedule
Date: 07-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

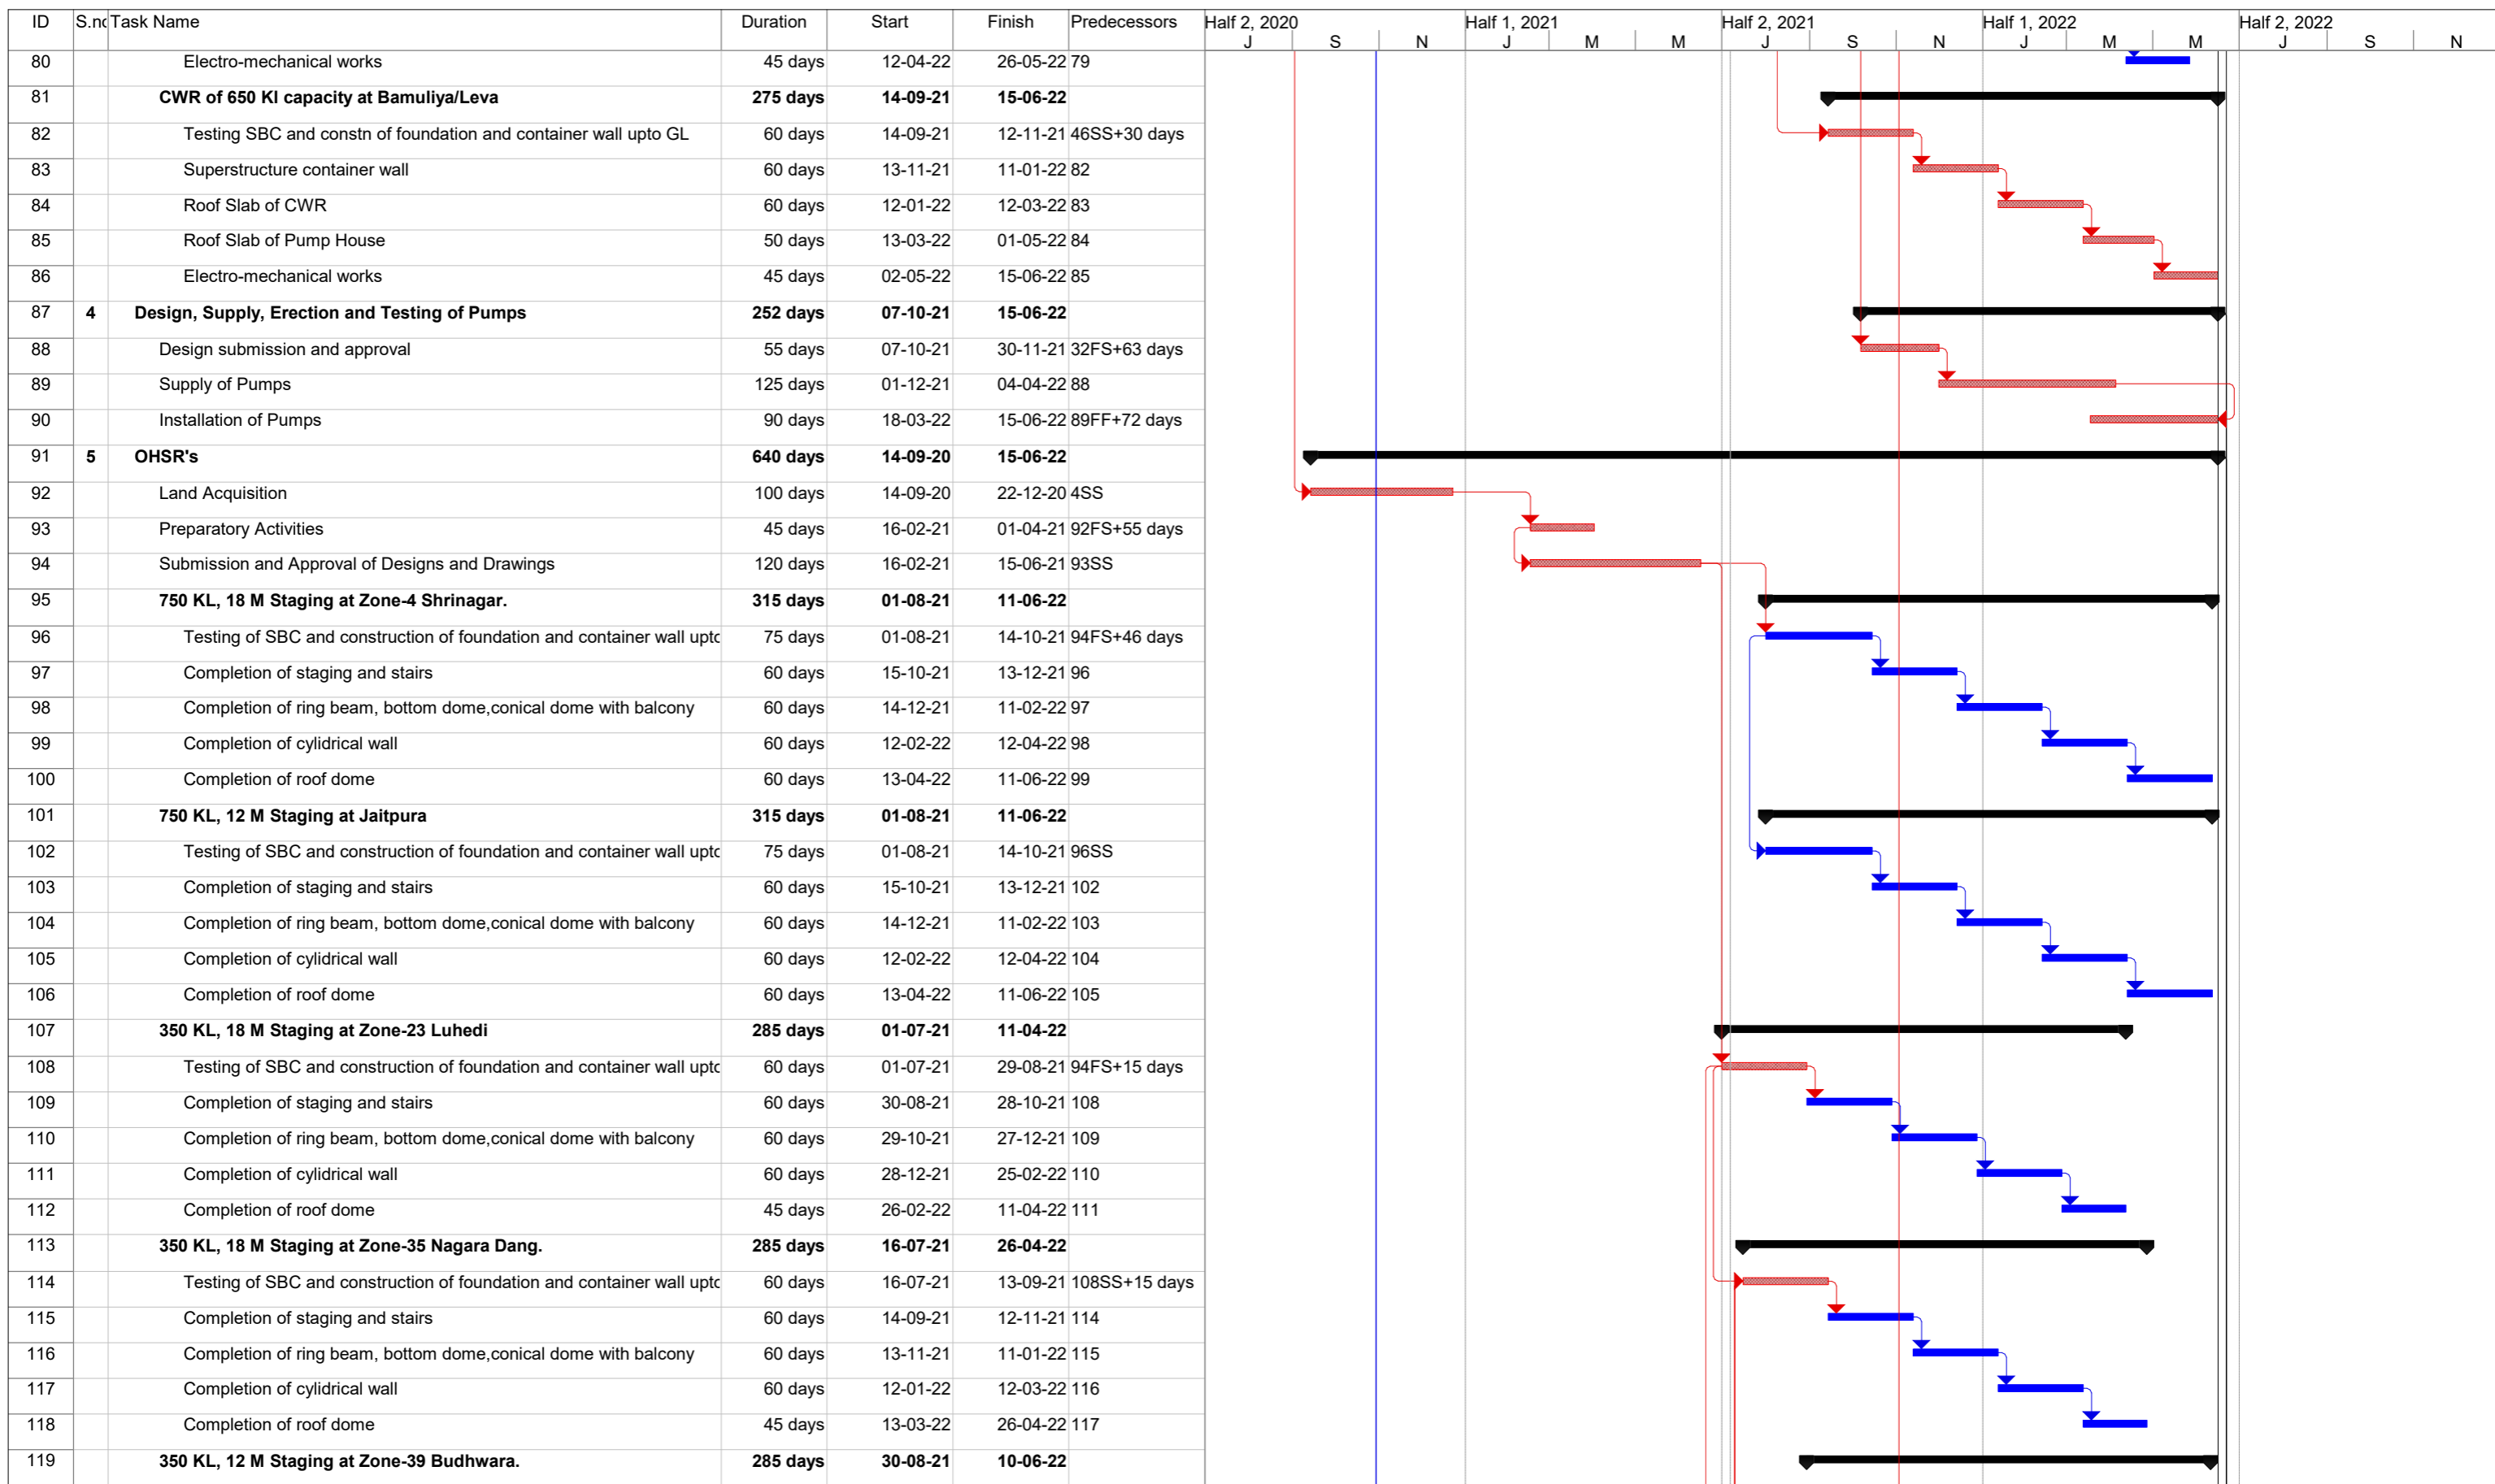

Project: Jhilo Construction Schedule Date: 07-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

ID	S.nc	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022								
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N						
120		Testing of SBC and construction of foundation and container wall upto	60 days	30-08-21	28-10-21	114SS+45 days																					
121		Completion of staging and stairs	60 days	29-10-21	27-12-21	120																					
122		Completion of ring beam, bottom dome, conical dome with balcony	60 days	28-12-21	25-02-22	121																					
123		Completion of cylindrical wall	60 days	26-02-22	26-04-22	122																					
124		Completion of roof dome	45 days	27-04-22	10-06-22	123																					
125		350 KL, 10 M Staging at Zone-13 Tolasoyam	285 days	01-07-21	11-04-22																						
126		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	108SS																					
127		Completion of staging and stairs	60 days	30-08-21	28-10-21	126																					
128		Completion of ring beam, bottom dome, conical dome with balcony	60 days	29-10-21	27-12-21	127																					
129		Completion of cylindrical wall	60 days	28-12-21	25-02-22	128																					
130		Completion of roof dome	45 days	26-02-22	11-04-22	129																					
131		350 KL, 10 M Staging at Mudhari	285 days	05-08-21	16-05-22																						
132		Testing of SBC and construction of foundation and container wall upto	60 days	05-08-21	03-10-21	114SS+20 days																					
133		Completion of staging and stairs	60 days	04-10-21	02-12-21	132																					
134		Completion of ring beam, bottom dome, conical dome with balcony	60 days	03-12-21	31-01-22	133																					
135		Completion of cylindrical wall	60 days	01-02-22	01-04-22	134																					
136		Completion of roof dome	45 days	02-04-22	16-05-22	135																					
137		300 KL, 20 M Staging at Zone-7 Basora.	270 days	01-07-21	27-03-22																						
138		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	126SS																					
139		Completion of staging and stairs	60 days	30-08-21	28-10-21	138																					
140		Completion of ring beam, bottom dome, conical dome with balcony	60 days	29-10-21	27-12-21	139																					
141		Completion of cylindrical wall	45 days	28-12-21	10-02-22	140																					
142		Completion of roof dome	45 days	11-02-22	27-03-22	141																					
143		300 KL, 18 M Staging at Zone-2 Dikwaha	270 days	01-07-21	27-03-22																						
144		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	138SS																					
145		Completion of staging and stairs	60 days	30-08-21	28-10-21	144																					
146		Completion of ring beam, bottom dome, conical dome with balcony	60 days	29-10-21	27-12-21	145																					
147		Completion of cylindrical wall	45 days	28-12-21	10-02-22	146																					
148		Completion of roof dome	45 days	11-02-22	27-03-22	147																					
149		300 KL, 18 M Staging at Zone-41 Dhawarra/Dharampura,	270 days	30-08-21	26-05-22																						
150		Testing of SBC and construction of foundation and container wall upto	60 days	30-08-21	28-10-21	120SS																					
151		Completion of staging and stairs	60 days	29-10-21	27-12-21	150																					
152		Completion of ring beam, bottom dome, conical dome with balcony	60 days	28-12-21	25-02-22	151																					
153		Completion of cylindrical wall	45 days	26-02-22	11-04-22	152																					
154		Completion of roof dome	45 days	12-04-22	26-05-22	153																					
155		300 KL, 16 M Staging at Zone-27 Mahua Bandh	270 days	01-07-21	27-03-22																						
156		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	144SS																					
157		Completion of staging and stairs	60 days	30-08-21	28-10-21	156																					
158		Completion of ring beam, bottom dome, conical dome with balcony	60 days	29-10-21	27-12-21	157																					
159		Completion of cylindrical wall	45 days	28-12-21	10-02-22	158																					

Project: Jhilo Construction Schedule Date: 07-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
160		Completion of roof dome	45 days	11-02-22	27-03-22	159																
161		300 KL, 10 M Staging at Zone-12 Bilkhi	270 days	19-09-21	15-06-22																	
162		Testing of SBC and construction of foundation and container wall upto	60 days	19-09-21	17-11-21	150SS+20 days																
163		Completion of staging and stairs	60 days	18-11-21	16-01-22	162																
164		Completion of ring beam, bottom dome, conical dome with balcony	60 days	17-01-22	17-03-22	163																
165		Completion of cylindrical wall	45 days	18-03-22	01-05-22	164																
166		Completion of roof dome	45 days	02-05-22	15-06-22	165																
167		300 KL, 10 M Staging at Zone-30 Bamuliya/Leva	270 days	30-08-21	26-05-22																	
168		Testing of SBC and construction of foundation and container wall upto	60 days	30-08-21	28-10-21	150SS																
169		Completion of staging and stairs	60 days	29-10-21	27-12-21	168																
170		Completion of ring beam, bottom dome, conical dome with balcony	60 days	28-12-21	25-02-22	169																
171		Completion of cylindrical wall	45 days	26-02-22	11-04-22	170																
172		Completion of roof dome	45 days	12-04-22	26-05-22	171																
173		250 KL, 20 M Staging at Zone-5 Bhandara.	240 days	01-07-21	25-02-22																	
174		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	156SS																
175		Completion of staging and stairs	45 days	30-08-21	13-10-21	174																
176		Completion of ring beam, bottom dome, conical dome with balcony	45 days	14-10-21	27-11-21	175																
177		Completion of cylindrical wall	45 days	28-11-21	11-01-22	176																
178		Completion of roof dome	45 days	12-01-22	25-02-22	177																
179		250 KL, 18 M Staging at Zone-24 Atrar Maf	240 days	01-07-21	25-02-22																	
180		Testing of SBC and construction of foundation and container wall upto	60 days	01-07-21	29-08-21	174SS																
181		Completion of staging and stairs	45 days	30-08-21	13-10-21	180																
182		Completion of ring beam, bottom dome, conical dome with balcony	45 days	14-10-21	27-11-21	181																
183		Completion of cylindrical wall	45 days	28-11-21	11-01-22	182																
184		Completion of roof dome	45 days	12-01-22	25-02-22	183																
185		250 KL, 16 M Staging at Digaria	240 days	19-09-21	16-05-22																	
186		Testing of SBC and construction of foundation and container wall upto	60 days	19-09-21	17-11-21	162SS																
187		Completion of staging and stairs	45 days	18-11-21	01-01-22	186																
188		Completion of ring beam, bottom dome, conical dome with balcony	45 days	02-01-22	15-02-22	187																
189		Completion of cylindrical wall	45 days	16-02-22	01-04-22	188																
190		Completion of roof dome	45 days	02-04-22	16-05-22	189																
191		200 KL, 18 M Staging at Zone-34 Ari.	225 days	26-09-21	08-05-22																	
192		Testing of SBC and construction of foundation and container wall upto	45 days	26-09-21	09-11-21	186SS+7 days																
193		Completion of staging and stairs	45 days	10-11-21	24-12-21	192																
194		Completion of ring beam, bottom dome, conical dome with balcony	45 days	25-12-21	07-02-22	193																
195		Completion of cylindrical wall	45 days	08-02-22	24-03-22	194																
196		Completion of roof dome	45 days	25-03-22	08-05-22	195																
197		200 KL, 15 M Staging at Zone-28 Kaithaura / Akauni	225 days	01-07-21	10-02-22																	
198		Testing of SBC and construction of foundation and container wall upto	45 days	01-07-21	14-08-21	180SS																
199		Completion of staging and stairs	45 days	15-08-21	28-09-21	198																

Project: Jhilo Construction Schedule
Date: 07-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022				
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N		
200		Completion of ring beam, bottom dome, conical dome with balcony	45 days	29-09-21	12-11-21	199																	
201		Completion of cylindrical wall	45 days	13-11-21	27-12-21	200																	
202		Completion of roof dome	45 days	28-12-21	10-02-22	201																	
203		200 KL, 10 M Staging at Zone-14 Swasa Maf	225 days	01-08-21	13-03-22																		
204		Testing of SBC and construction of foundation and container wall upto	45 days	01-08-21	14-09-21	198SS+31 days																	
205		Completion of staging and stairs	45 days	15-09-21	29-10-21	204																	
206		Completion of ring beam, bottom dome, conical dome with balcony	45 days	30-10-21	13-12-21	205																	
207		Completion of cylindrical wall	45 days	14-12-21	27-01-22	206																	
208		Completion of roof dome	45 days	28-01-22	13-03-22	207																	
209		150 KL, 15 M Staging at Zone-18 Thathewra	195 days	18-08-21	28-02-22																		
210		Testing of SBC and construction of foundation and container wall upto	45 days	18-08-21	01-10-21	132SS+13 days																	
211		Completion of staging and stairs	45 days	02-10-21	15-11-21	210																	
212		Completion of ring beam, bottom dome, conical dome with balcony	45 days	16-11-21	30-12-21	211																	
213		Completion of cylindrical wall	30 days	31-12-21	29-01-22	212																	
214		Completion of roof dome	30 days	30-01-22	28-02-22	213																	
215		150 KL, 12 M Staging at Zone-10 Rahelia	195 days	30-07-21	09-02-22																		
216		Testing of SBC and construction of foundation and container wall upto	45 days	30-07-21	12-09-21	114SS+14 days																	
217		Completion of staging and stairs	45 days	13-09-21	27-10-21	216																	
218		Completion of ring beam, bottom dome, conical dome with balcony	45 days	28-10-21	11-12-21	217																	
219		Completion of cylindrical wall	30 days	12-12-21	10-01-22	218																	
220		Completion of roof dome	30 days	11-01-22	09-02-22	219																	
221		150 KL, 10 M Staging at Pach Pahra	195 days	01-09-21	14-03-22																		
222		Testing of SBC and construction of foundation and container wall upto	45 days	01-09-21	15-10-21	204SS+31 days																	
223		Completion of staging and stairs	45 days	16-10-21	29-11-21	222																	
224		Completion of ring beam, bottom dome, conical dome with balcony	45 days	30-11-21	13-01-22	223																	
225		Completion of cylindrical wall	30 days	14-01-22	12-02-22	224																	
226		Completion of roof dome	30 days	13-02-22	14-03-22	225																	
227		100 KL, 18 M Staging at Zone-25 Dudhaiya	165 days	01-10-21	14-03-22																		
228		Testing of SBC and construction of foundation and container wall upto	45 days	01-10-21	14-11-21	222SS+30 days																	
229		Completion of staging and stairs	30 days	15-11-21	14-12-21	228																	
230		Completion of ring beam, bottom dome, conical dome with balcony	30 days	15-12-21	13-01-22	229																	
231		Completion of cylindrical wall	30 days	14-01-22	12-02-22	230																	
232		Completion of roof dome	30 days	13-02-22	14-03-22	231																	
233		100 KL, 12 M Staging at Zone-40 Ghaghaura .	165 days	29-08-21	09-02-22																		
234		Testing of SBC and construction of foundation and container wall upto	45 days	29-08-21	12-10-21	216SS+30 days																	
235		Completion of staging and stairs	30 days	13-10-21	11-11-21	234																	
236		Completion of ring beam, bottom dome, conical dome with balcony	30 days	12-11-21	11-12-21	235																	
237		Completion of cylindrical wall	30 days	12-12-21	10-01-22	236																	
238		Completion of roof dome	30 days	11-01-22	09-02-22	237																	
239		100 KL, 10 M Staging at Zone-42 Narwara	165 days	29-08-21	09-02-22																		

Project: Jhilo Construction Schedule
Date: 07-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

ID	S.nc	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
240		Testing of SBC and construction of foundation and container wall upto	45 days	29-08-21	12-10-21	234SS																
241		Completion of staging and stairs	30 days	13-10-21	11-11-21	240																
242		Completion of ring beam, bottom dome, conical dome with balcony	30 days	12-11-21	11-12-21	241																
243		Completion of cylindrical wall	30 days	12-12-21	10-01-22	242																
244		Completion of roof dome	30 days	11-01-22	09-02-22	243																
245		100 KL, 10 M Staging at Zone-43 Sigaun	165 days	18-09-21	01-03-22																	
246		Testing of SBC and construction of foundation and container wall upto	45 days	18-09-21	01-11-21	240SS+20 days																
247		Completion of staging and stairs	30 days	02-11-21	01-12-21	246																
248		Completion of ring beam, bottom dome, conical dome with balcony	30 days	02-12-21	31-12-21	247																
249		Completion of cylindrical wall	30 days	01-01-22	30-01-22	248																
250		Completion of roof dome	30 days	31-01-22	01-03-22	249																
251		100 KL, 10 M Staging at Chittarwara	165 days	05-09-21	16-02-22																	
252		Testing of SBC and construction of foundation and container wall upto	45 days	05-09-21	19-10-21	240SS+7 days																
253		Completion of staging and stairs	30 days	20-10-21	18-11-21	252																
254		Completion of ring beam, bottom dome, conical dome with balcony	30 days	19-11-21	18-12-21	253																
255		Completion of cylindrical wall	30 days	19-12-21	17-01-22	254																
256		Completion of roof dome	30 days	18-01-22	16-02-22	255																
257		75 KL, 10 M Staging, at Zone-22 Karpahariya	150 days	05-09-21	01-02-22																	
258		Testing of SBC and construction of foundation and container wall upto	30 days	05-09-21	04-10-21	252SS																
259		Completion of staging and stairs	30 days	05-10-21	03-11-21	258																
260		Completion of ring beam, bottom dome, conical dome with balcony	30 days	04-11-21	03-12-21	259																
261		Completion of cylindrical wall	30 days	04-12-21	02-01-22	260																
262		Completion of roof dome	30 days	03-01-22	01-02-22	261																
263		50 KL, 10 M Staging, at Zone-31 Saithwara.	150 days	25-09-21	21-02-22																	
264		Testing of SBC and construction of foundation and container wall upto	30 days	25-09-21	24-10-21	258SS+20 days																
265		Completion of staging and stairs	30 days	25-10-21	23-11-21	264																
266		Completion of ring beam, bottom dome, conical dome with balcony	30 days	24-11-21	23-12-21	265																
267		Completion of cylindrical wall	30 days	24-12-21	22-01-22	266																
268		Completion of roof dome	30 days	23-01-22	21-02-22	267																
269	7	Pipeline works	540 days	20-12-20	12-06-22																	
270		Submission and Approval of Hydraulic Designs and Drawings	200 days	20-12-20	07-07-21	7SS+45 days																
271		Pipe Delivery at Site after inspection	450 days	18-02-21	13-05-22	270SS+60 days																
272		Laying and Jointing	320 days	15-07-21	30-05-22																	
273		DI Pipe Laying	300 days	02-08-21	28-05-22	271SS+165 days																
274		HDPE Pipe Laying	320 days	15-07-21	30-05-22	270FS+7 days																
275		GI Pipe Laying	145 days	01-01-22	25-05-22	273SS+152 days																
276		Sectional Testing	270 days	16-09-21	12-06-22	273SS+45 days																
277	8	Supply of Sluice and Scour Valves	230 days	01-10-21	18-05-22																	
278		Supply	150 days	01-10-21	27-02-22	273SS+60 days																
279		Erection	200 days	31-10-21	18-05-22	278SS+30 days																


Project: Jhilo Construction Schedule Date: 07-07-21	Critical		Baseline		Project Summary		Duration-only		External Milestone	
	Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
	Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
	Task		Milestone		Inactive Milestone		Start-only			
	Split		Summary Progress		Inactive Summary		Finish-only			
	Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
280	9	Supply & Laying of Fire Hydrant - 101 No's	195 days	01-12-21	13-06-22																	
281		Supply	60 days	01-12-21	29-01-22	278SS+61 days																
282		Erection	165 days	31-12-21	13-06-22	281SS+30 days																
283	10	Non return valves - 14 No's	105 days	30-01-22	14-05-22																	
284		Supply	60 days	30-01-22	30-03-22	281																
285		Erection	75 days	01-03-22	14-05-22	284SS+30 days																
286	11	Air Valves - 1023 No's	225 days	01-11-21	13-06-22																	
287		Supply	60 days	01-11-21	30-12-21	278SS+31 days																
288		Erection	195 days	01-12-21	13-06-22	287SS+30 days																
289	12	Supply & Laying of Air Valves (20 mm dia DI/DF)	225 days	01-11-21	13-06-22																	
290		Supply	60 days	01-11-21	30-12-21	278SS+31 days																
291		Erection	195 days	01-12-21	13-06-22	290SS+30 days																
292	13	Construction of Chambers	355 days	06-09-21	26-08-22																	
293		Submission and Approval of Designs and Drawings	75 days	06-09-21	19-11-21	270FS+60 days																
294		Construction	280 days	20-11-21	26-08-22	293																
295	14	Construction of Thrust Blocks	280 days	06-09-21	12-06-22																	
296		Submission and Approval of Designs and Drawings	60 days	06-09-21	04-11-21	293SS																
297		Construction	220 days	05-11-21	12-06-22	296																
298	15	Dismantling of Road Surfaces	190 days	05-11-21	13-05-22	296																
299	16	Restoration of Road Surfaces	190 days	05-12-21	12-06-22	298SS+30 days																
300	17	Construction of single tap PTSP	185 days	01-12-21	03-06-22																	
301		Submission and Approval of Designs and Drawings	60 days	01-12-21	29-01-22	270FS+146 days																
302		Supply & Erection	125 days	30-01-22	03-06-22	301																
303	18	Nala/Culvert/Road Crossings	280 days	22-08-21	28-05-22																	
304		Submission and Approval of Designs and Drawings	60 days	22-08-21	20-10-21	270FS+45 days																
305		Construction	220 days	21-10-21	28-05-22	304																
306	19	Trenchless Crossing of National/ State Highway Road and Railway Trac	275 days	22-08-21	23-05-22																	
307		Submission and Approval of Designs and Drawings	75 days	22-08-21	04-11-21	304SS																
308		Construction	200 days	05-11-21	23-05-22	307																
309	20	Making House Connections	250 days	06-10-21	12-06-22																	
310		Submission and Approval of Designs and Drawings	60 days	06-10-21	04-12-21	270FS+90 days																
311		Supply & Erection	190 days	05-12-21	12-06-22	310																
312	21	Construction of Boundary wall	415 days	04-01-21	22-02-22																	
313		Submission and Approval of Designs and Drawings	75 days	04-01-21	19-03-21	7SS+60 days																
314		Construction	340 days	20-03-21	22-02-22	313																
315	27	Single Staff Quarters	245 days	06-10-21	07-06-22																	
316		Submission and Approval of Designs and Drawings	45 days	06-10-21	19-11-21	270FS+90 days																
317		Construction	200 days	20-11-21	07-06-22	316																
318	31	Electromagnetic FM - 47 No's	205 days	03-11-21	26-05-22																	

Project: Jhilo Construction Schedule
Date: 07-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			

ID	S.no	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2020			Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			
							J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	
319		Supply	45 days	03-11-21	17-12-21	32FS+90 days																
320		Erection	160 days	18-12-21	26-05-22	319																
321	32	Chlorinating System-	145 days	02-01-22	26-05-22																	
322		Supply	45 days	02-01-22	15-02-22	319FS+15 days																
323		Erection	100 days	16-02-22	26-05-22	322																
324	34	Electric Transformer	136 days	02-01-22	17-05-22																	
325		Supply	110 days	02-01-22	21-04-22	319FS+15 days																
326		Erection	80 days	27-02-22	17-05-22	325SS+56 days																
327	35	Diesel Generating Sets	165 days	02-01-22	15-06-22																	
328		Supply	45 days	02-01-22	15-02-22	325SS																
329		Erection	120 days	16-02-22	15-06-22	328																
330	36	Supply and Installation of LT Cable from DG set to LT Panel	165 days	02-01-22	15-06-22																	
331		Supply	45 days	02-01-22	15-02-22	328SS																
332		Erection	120 days	16-02-22	15-06-22	331																
333		Trail Run and Commissioning	90 days	16-06-22	13-09-22	8,13,30,87,91,26																

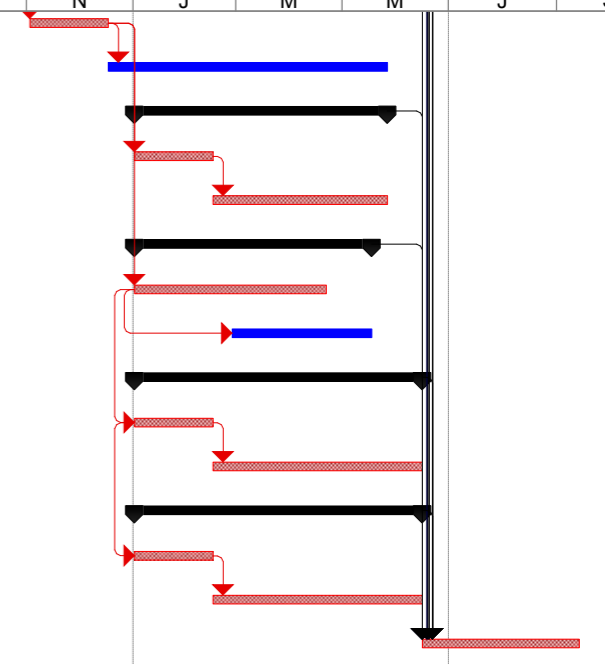

Project: Jhilo Construction Schedule
Date: 07-07-21

Critical		Baseline		Project Summary		Duration-only		External Milestone	
Critical Split		Baseline Split		External Tasks		Manual Summary Rollup		Deadline	
Critical Progress		Baseline Milestone		External Milestone		Manual Summary			
Task		Milestone		Inactive Milestone		Start-only			
Split		Summary Progress		Inactive Summary		Finish-only			
Task Progress		Summary		Manual Task		External Tasks			
