


Project: Gulara Project Planning S	Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress
	Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline		
	Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress		

						NCC LIMITED- Project: Gulara, Bachouli & Tilaetha Group of Villages															
ID	Task Mode	Task Name	Duration	Start	Finish	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	2022 Jan	Feb	Mar	Apr	May	Jun	Jul	
237		Complete- Bottom dome, Cylind	45 days	Wed 15-09-21	Fri 29-10-21																
238		Complete Cone Wall & Top Roof	45 days	Sat 30-10-21	Mon 13-12-21																
239		Erection of Mechanical Fitting	10 days	Tue 14-12-21	Thu 23-12-21																
240		Testing	7 days	Fri 24-12-21	Thu 30-12-21																
241		PSP & House Service Connection	240 days	Sun 01-08-21	Mon 28-03-22																
242		PSP & aligned items	240 days	Sun 01-08-21	Mon 28-03-22																
243		House Connection & aligned iter	240 days	Sun 01-08-21	Mon 28-03-22																
244		Misc Civil Works	300 days	Wed 02-06-21	Mon 28-03-22																
245		Staff Quarter	210 days	Wed 02-06-21	Tue 28-12-21																
246		Boundary wall	210 days	Wed 02-06-21	Tue 28-12-21																
247		MS Gate	180 days	Sun 01-08-21	Thu 27-01-22																
248		Restoration Work	240 days	Sun 01-08-21	Mon 28-03-22																
249		Drain	120 days	Mon 29-11-21	Mon 28-03-22																
250		Earth Filling	60 days	Fri 28-01-22	Mon 28-03-22																
251		Tilaetha Group of Villages	303 days	Wed 02-06-21	Thu 31-03-22																
252		Intake- Tilaetha (Betwa River)	300 days	Wed 02-06-21	Mon 28-03-22																
253		Construction of coffer dam, excavation of foundation and casting of bed concrete & fabrication of shuttering	45 days	Wed 02-06-21	Fri 16-07-21																
254		Completing foundation and well staining up-to discharge floor level.	80 days	Sat 17-07-21	Mon 04-10-21																
255		Construction of R.C.C. approach bridge, approach road and discharge	75 days	Tue 05-10-21	Sat 18-12-21																
256		Completing pump house up to roof slab with bridge connecting jack well with intake, R.C.C. Duct conduit etc.	60 days	Sun 19-12-21	Wed 16-02-22																
257		Electro-mechanical Work	40 days	Thu 17-02-22	Mon 28-03-22																
258		WTP 08 MLD- Tilaetha	300 days	Wed 02-06-21	Mon 28-03-22																
259		Cascade aerator/Inlet chamber	45 days	Tue 22-06-21	Thu 05-08-21																
260		Flash Mixer with inlet channel	40 days	Fri 06-08-21	Tue 14-09-21																
261		Pre-setting tank and/or Clariflocculato	180 days	Wed 02-06-21	Sun 28-11-21																
262		Filters	90 days	Thu 30-09-21	Tue 28-12-21																
263		Wash Water Tank	60 days	Thu 30-09-21	Sun 28-11-21																
264		Administrative Block	120 days	Wed 02-06-21	Wed 29-09-21																
265		Lab Building	120 days	Wed 02-06-21	Wed 29-09-21																
266		Store Building	120 days	Wed 02-06-21	Wed 29-09-21																
267		Clear Water Sump	90 days	Thu 30-09-21	Tue 28-12-21																
268		Clear Water Pump House	210 days	Fri 02-07-21	Thu 27-01-22																
269		Electro-mechanical Work	60 days	Fri 28-01-22	Mon 28-03-22																
270		Boundary wall	210 days	Wed 02-06-21	Tue 28-12-21																
271		Roads work of campus	45 days	Wed 29-12-21	Fri 11-02-22																
272		Site development and etc.	30 days	Sat 12-02-22	Sun 13-03-22																
273		RAW Water Piping	110 days	Wed 02-06-21	Sun 19-09-21																
274		Supply of DI Pipe & Fitting	45 days	Wed 02-06-21	Fri 16-07-21																
275		Laying, Jointing & Backfilling	90 days	Wed 02-06-21	Mon 30-08-21																
276		Construction of Thrust Block & Chamb	30 days	Sun 01-08-21	Mon 30-08-21																
277		Erection of Mechanical Fitting	20 days	Tue 31-08-21	Sun 19-09-21																
278		Clear Water Rising Main	235 days	Wed 02-06-21	Sat 22-01-22																
279		Supply of Pipe & Fittings	120 days	Wed 02-06-21	Wed 29-09-21																
280		Supply of Valves (SV,Sch,AV,FH)	60 days	Thu 30-09-21	Sun 28-11-21																
281		Laying, Jointing & Backfilling	150 days	Wed 02-06-21	Fri 29-10-21																
282		Sectional Hydrotesting	150 days	Fri 02-07-21	Sun 28-11-21																
283		Construction of Thrust Blocks & Cf	45 days	Tue 09-11-21	Thu 23-12-21																
284		Erection of Valves (SV,Sch,AV,FH)	45 days	Thu 09-12-21	Sat 22-01-22																
285		CWR Cum Pump House	215 days	Fri 02-07-21	Tue 01-02-22																
286		Supply of Mechanical and Electric	60 days	Thu 30-09-21	Sun 28-11-21																
287		300 KL Cap cum PH- Tendol (CWR)	190 days	Fri 02-07-21	Fri 07-01-22																
288		Upto GL of Container Wall	30 days	Fri 02-07-21	Sat 31-07-21																
289		Super Structure & Walls	45 days	Sun 01-08-21	Tue 14-09-21																
290		Roof Slab of CWR	30 days	Wed 15-09-21	Thu 14-10-21																
291		Roof Slab of Pump House	45 days	Fri 15-10-21	Sun 28-11-21																
292		Electro-mechanical Work	30 days	Mon 29-11-21	Tue 28-12-21																
293		Testing	10 days	Wed 29-12-21	Fri 07-01-22																
294		250 KL Cap cum PH- Ujayan (CWR)	215 days	Fri 02-07-21	Tue 01-02-22																
295		Upto GL of Container Wall	40 days	Fri 02-07-21	Tue 10-08-21																

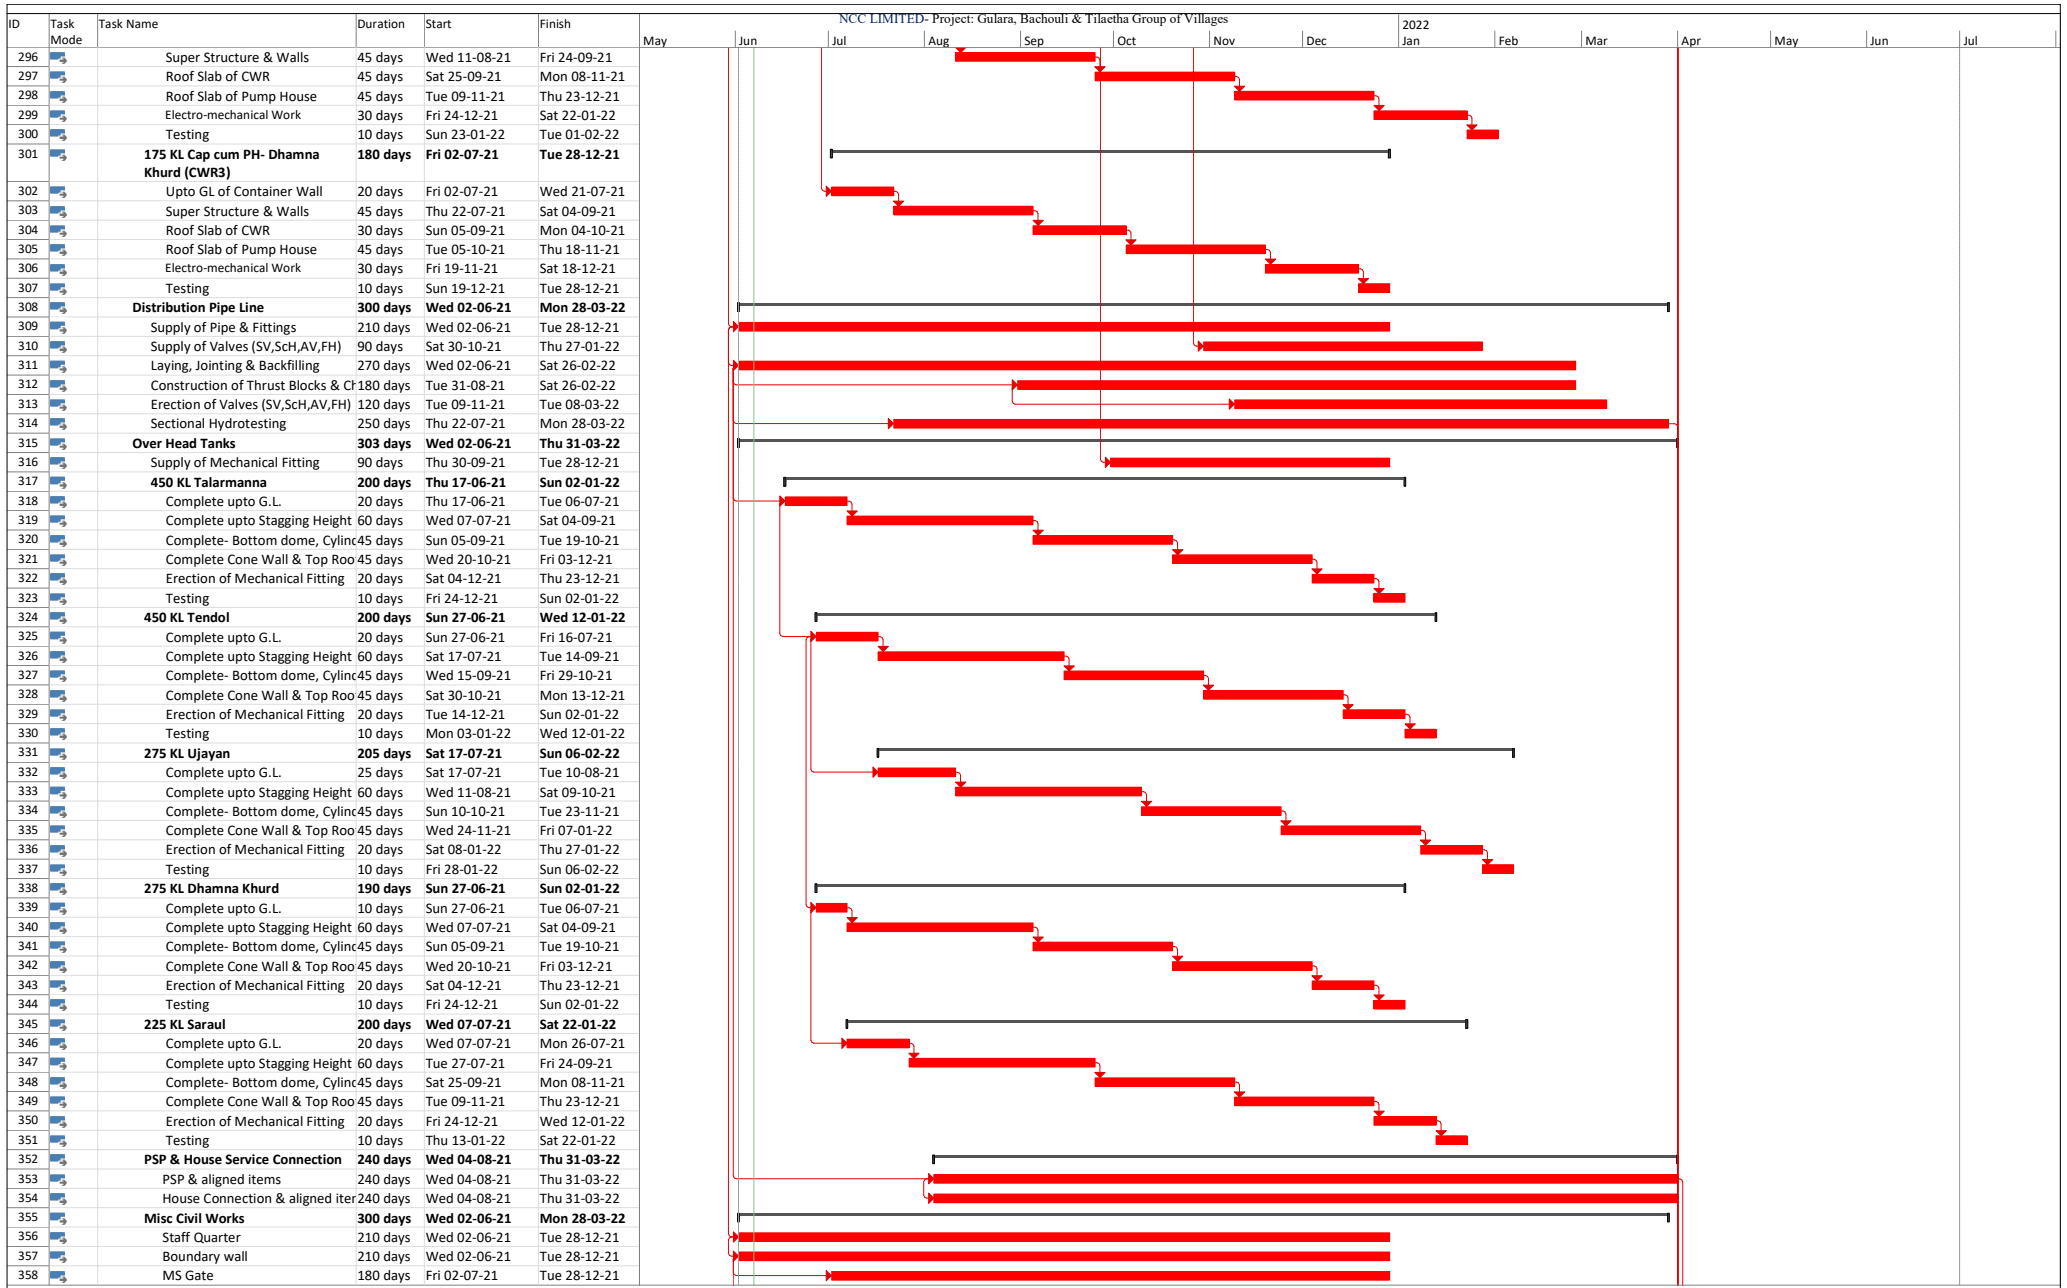

Project: Gulara Project Planning S

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

						NCC LIMITED- Project: Gulara, Bachouli & Tilaetha Group of Villages															
ID	Task Mode	Task Name	Duration	Start	Finish	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	2022 Jan	Feb	Mar	Apr	May	Jun	Jul	
359		Restoration Work	240 days	Sun 01-08-21	Mon 28-03-22																
360		Drain	120 days	Wed 15-09-21	Wed 12-01-22																
361		Earth Filling	60 days	Tue 14-12-21	Fri 11-02-22																
362		Trail Run	91 days	Fri 01-04-22	Thu 30-06-22																
363		GI pipe laying in narrow street of villages	91 days	Fri 01-04-22	Thu 30-06-22																
364		House Connection & aligned items	91 days	Fri 01-04-22	Thu 30-06-22																
365		Other miscellaneous works etc.	91 days	Fri 01-04-22	Thu 30-06-22																

Project: Gulara Project Planning S	Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
	Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
	Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			
