


CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
1	Construction of Jakhlaun-Birdha Group of Villages Water Supply Scheme, District- Lalitpur, Uttar Pradesh	721 days	Fri 27-11-20	Mon 21-11-22																
2	LOA	1 day	Fri 27-11-20	Fri 27-11-20																
3	Agreement Date	1 day	Tue 08-12-20	Tue 08-12-20	2FS+10 days															
4	Mobilization of staff & office infrastructure	222 days	Sat 19-12-20	Fri 30-07-21	3FS+10 days															
5	Land Acquisition by client	214 days	Tue 29-12-20	Sun 01-08-21	3FS+20 days															
6	Geotechnical Investigation	86 days	Fri 08-01-21	Sun 04-04-21	5SS+10 days															
7	Pipeline Network finilization by client	42 days	Sat 19-12-20	Sat 30-01-21	3FS+10 days															
8	Detailed Survey Work	45 days	Thu 24-12-20	Sun 07-02-21	7SS+5 days															
9	Construction of Intake Well of minimum internal size of 7 M Dia & 22.67 M Clear Depth	589 days	Mon 08-02-21	Thu 22-09-22																
10	Handing over of encumbrance Free site by client	1 day	Mon 08-02-21	Mon 08-02-21	5SS+40 days															
11	Submission and approval of design & Drawings	118 days	Mon 05-04-21	Sun 01-08-21	6															
12	Construction of coffer dam, excavation of foundation and casting of bed concrete.	60 days	Mon 02-08-21	Fri 01-10-21	11															
13	Completing foundation and well staning up-to discharge floor level	190 days	Sun 03-10-21	Sun 10-04-22	12															
14	Construction of R.C.C. approach bridge, approach road and discharge floor	120 days	Thu 02-12-21	Thu 31-03-22	13SS+60 days															
15	Completing pump house up to roof slab with bridge connecting jack well with intake, R.C.C. Duct conduit including excavation of channel and laying infiltration gallery	90 days	Mon 11-04-22	Sat 09-07-22	13															
16	Mechanical Works	45 days	Sun 10-07-22	Tue 23-08-22	15															
17	Electrical Works	45 days	Sun 10-07-22	Tue 23-08-22	15															
18	Instrumentation works	25 days	Mon 29-08-22	Thu 22-09-22	17FF+30 days															
19	Finishing Works	40 days	Sun 10-07-22	Thu 18-08-22	15															
20	Construction of 20MLD Water Treatment Plant	580 days	Sun 14-02-21	Mon 19-09-22																
21	Handing over of encumbrance Free site by client	1 day	Sun 14-02-21	Sun 14-02-21	5SS+46 days															
22	Submission and approval of design & Drawings for	120 days	Mon 05-04-21	Tue 03-08-21	6															
23	Construction of cascade aerator/Inlet chamber	180 days	Tue 05-10-21	Sat 02-04-22	22FS+60 days															
24	Construction of Parshall Flume, Bypas Channel	120 days	Sat 04-12-21	Sat 02-04-22	23SS+60 days															
25	Construction of Flash Mixer with inlet channel	60 days	Sun 19-09-21	Thu 18-11-21	22FS+45 days															
26	Construction of Clarrifloculator	180 days	Sat 14-08-21	Fri 11-02-22	22FS+10 days															
27	Construction of Filter House cum Back wash Tank	280 days	Sat 14-08-21	Sun 22-05-22	22FS+10 days															
28	Construction of Wash Water Recovery Tank	180 days	Tue 05-10-21	Sat 02-04-22	22FS+60 days															
29	Construction of Administrative buildings with Control room	240 days	Sat 04-09-21	Mon 02-05-22	22FS+30 days															
30	Recycling Arrangement-Sludge Collection & Disposal , Backwash water disposal	150 days	Sat 04-12-21	Mon 02-05-22	22FS+120 days															
31	Construction of Chemical Building	120 days	Sat 04-12-21	Sat 02-04-22	22FS+120 days															



	Task		External Tasks		Manual Task		Finish-only
	Split		External Milestone		Duration-only		Deadline
	Milestone		Inactive Task		Manual Summary Rollup		Progress
	Summary		Inactive Milestone		Manual Summary		
	Project Summary		Inactive Summary		Start-only		

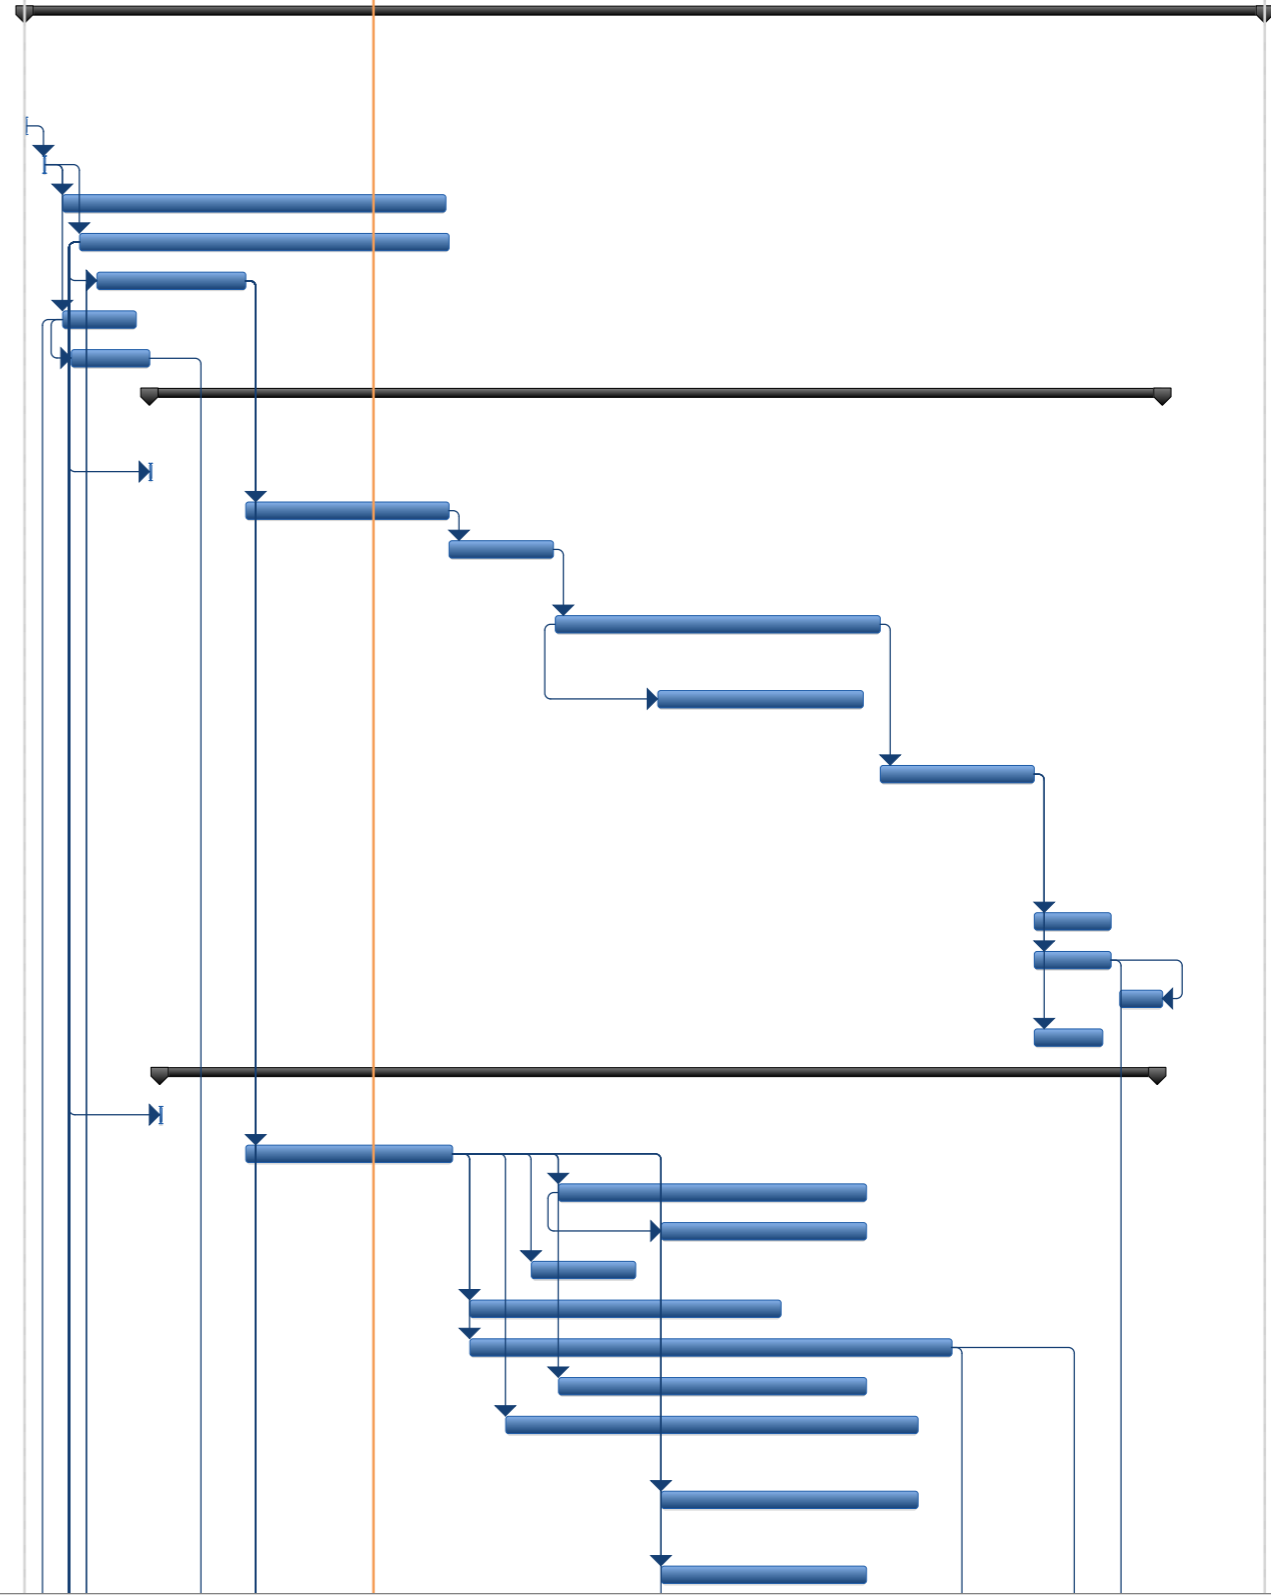

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
32	Construction of Chlorinating room	120 days	Sat 04-12-21	Sat 02-04-22	22FS+120 days																
33	Mechanical and Electrical works with Automation	60 days	Mon 23-05-22	Thu 21-07-22	27																
34	Roads work of campus	60 days	Mon 23-05-22	Thu 21-07-22	27FF+60 days																
35	Site development	60 days	Fri 22-07-22	Mon 19-09-22	34																
36	Construction of Clear Water Reservoir cum Pump Ho	544 days	Thu 21-01-21	Fri 22-07-22																	
37	Zone_1_CWR-1 at WTP of 1900 KL Capacity cum Pump House	521 days	Sun 14-02-21	Fri 22-07-22																	
38	Handing over of encumbrance Free site by client	1 day	Sun 14-02-21	Sun 14-02-21	5SS+46 days																
39	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
40	Construction of foundation and container wall upto GL	100 days	Wed 04-08-21	Sat 13-11-21	39FS+30 days																
41	Super structure container wall	30 days	Sun 14-11-21	Mon 13-12-21	40																
42	Roof structure	45 days	Tue 14-12-21	Thu 27-01-22	41																
43	Pipes and fittings	25 days	Fri 28-01-22	Mon 21-02-22	42																
44	Hydrotesting	60 days	Tue 22-02-22	Fri 22-04-22	43																
45	Pump House	176 days	Fri 28-01-22	Fri 22-07-22																	
46	columns up to lintel Beams	15 days	Fri 28-01-22	Fri 11-02-22	42																
47	Lintel Beam	14 days	Sat 12-02-22	Fri 25-02-22	46																
48	Columns above lintel beams up to top slab of Pump House	17 days	Sat 26-02-22	Mon 14-03-22	47																
49	Roof structure	30 days	Tue 15-03-22	Wed 13-04-22	48																
50	Brick Work,including plastering inside & outsi	60 days	Thu 14-04-22	Sun 12-06-22	49																
51	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	40 days	Mon 13-06-22	Fri 22-07-22	50																
52	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
53	Submission & Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	39																
54	Supply	90 days	Thu 04-11-21	Tue 01-02-22	53FS+90 days																
55	Mechanical Erection	60 days	Thu 17-02-22	Sun 17-04-22	42FS+20 days,5																
56	Electrical Works	45 days	Thu 17-02-22	Sat 02-04-22	42FS+20 days,5																
57	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	56																
58	Zone_6_CWR-2 of 200 KL Capacity cum Pump Hou	451 days	Sat 23-01-21	Fri 22-04-22																	
59	Handing over of encumbrance Free site by client	1 day	Sat 23-01-21	Sat 23-01-21	5SS+25 days																
60	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
61	Construction of foundation and container wall upto GL	60 days	Wed 04-08-21	Mon 04-10-21	60FS+30 days,59																
62	Super structure container wall	20 days	Tue 05-10-21	Sun 24-10-21	61																
63	Roof structure	30 days	Mon 25-10-21	Tue 23-11-21	62																
64	Pipes and fittings	20 days	Wed 24-11-21	Mon 13-12-21	63																
65	Hydrotesting	60 days	Tue 14-12-21	Fri 11-02-22	64																
66	Pump House	126 days	Wed 24-11-21	Tue 29-03-22																	



GAYATRI - RAMKY (P)
 6-3 10th Floor, Sector 10, Gurgaon, Haryana, India. Phone: 01292 221000, 01292 221001
 20114256, Fax: 0129 22100155



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
67	columns up to lintel Beams	10 days	Wed 24-11-21	Fri 03-12-21	63																
68	Lintel Beam	12 days	Sat 04-12-21	Wed 15-12-21	67																
69	Columns above lintel beams up to top slab of Pump House	14 days	Thu 16-12-21	Wed 29-12-21	68																
70	Roof structure	25 days	Thu 30-12-21	Sun 23-01-22	69																
71	Brick Work,including plastering inside & outsi	35 days	Mon 24-01-22	Sun 27-02-22	70																
72	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Mon 28-02-22	Tue 29-03-22	71																
73	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
74	Submission& Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	60																
75	Supply	120 days	Thu 04-11-21	Thu 03-03-22	74FS+90 days																
76	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	75,70FS+20 day																
77	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	75,70FS+20 day																
78	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	77																
79	Zone_2_CWR-3 of 200 KL Capacity cum Pump Hou	434 days	Wed 10-02-21	Fri 22-04-22																	
80	Handing over of encumbrance Free site by client	1 day	Wed 10-02-21	Wed 10-02-21	5SS+42 days																
81	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
82	Construction of foundation and container wall upto GL	60 days	Sun 25-07-21	Thu 23-09-21	80,81FS+20 days																
83	Super structure container wall	20 days	Fri 24-09-21	Thu 14-10-21	82																
84	Roof structure	30 days	Fri 15-10-21	Sat 13-11-21	83																
85	Pipes and fittings	20 days	Sun 14-11-21	Fri 03-12-21	84																
86	Hydrotesting	60 days	Sat 04-12-21	Tue 01-02-22	85																
87	Pump House	126 days	Sun 14-11-21	Sat 19-03-22																	
88	columns up to lintel Beams	10 days	Sun 14-11-21	Tue 23-11-21	84																
89	Lintel Beam	12 days	Wed 24-11-21	Sun 05-12-21	88																
90	Columns above lintel beams up to top slab of Pump House	14 days	Mon 06-12-21	Sun 19-12-21	89																
91	Roof structure	25 days	Mon 20-12-21	Thu 13-01-22	90																
92	Brick Work,including plastering inside & outsi	35 days	Fri 14-01-22	Thu 17-02-22	91																
93	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Fri 18-02-22	Sat 19-03-22	92																
94	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
95	Submission& Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	81																
96	Supply	120 days	Thu 04-11-21	Thu 03-03-22	95FS+90 days																
97	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	91FS+20 days,9																
98	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	96,91FS+20 day																
99	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	98																
100	Zone_4_CWR-4 of 100 KL Capacity cum Pump Hou	453 days	Thu 21-01-21	Fri 22-04-22																	
101	Handing over of encumbrance Free site by client	1 day	Thu 21-01-21	Thu 21-01-21	5SS+23 days																



GAYATRI - RAMKY (P)
6-3 10th Floor, Sector 10, Gurgaon, Haryana, India. Tel: 0124-2311426, Fax: 0124-2311415



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
102	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
103	Construction of foundation and container wall upto GL	50 days	Sun 25-07-21	Mon 13-09-21	101,102FS+20 days																
104	Super structure container wall	18 days	Tue 14-09-21	Fri 01-10-21	103																
105	Roof structure	30 days	Sun 03-10-21	Mon 01-11-21	104																
106	Pipes and fittings	20 days	Tue 02-11-21	Sun 21-11-21	105																
107	Hydrotesting	60 days	Mon 22-11-21	Thu 20-01-22	106																
108	Pump House	116 days	Tue 02-11-21	Fri 25-02-22																	
109	columns up to lintel Beams	10 days	Tue 02-11-21	Thu 11-11-21	105																
110	Lintel Beam	12 days	Fri 12-11-21	Tue 23-11-21	109																
111	Columns above lintel beams up to top slab of Pump House	14 days	Wed 24-11-21	Tue 07-12-21	110																
112	Roof structure	20 days	Wed 08-12-21	Mon 27-12-21	111																
113	Brick Work,including plastering inside & outside	30 days	Tue 28-12-21	Wed 26-01-22	112																
114	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Thu 27-01-22	Fri 25-02-22	113																
115	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
116	Submission & Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	102																
117	Supply	120 days	Thu 04-11-21	Thu 03-03-22	116FS+90 days																
118	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	112FS+20 days,																
119	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	117,112FS+20 c																
120	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	119																
121	Zone_5_CWR-5 of 100 KL Capacity cum Pump Hou	433 days	Thu 11-02-21	Fri 22-04-22																	
122	Handing over of encumbrance Free site by client	1 day	Thu 11-02-21	Thu 11-02-21	5SS+43 days																
123	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
124	Construction of foundation and container wall upto GL	50 days	Wed 04-08-21	Thu 23-09-21	122,123FS+30 days																
125	Super structure container wall	18 days	Fri 24-09-21	Tue 12-10-21	124																
126	Roof structure	30 days	Wed 13-10-21	Thu 11-11-21	125																
127	Pipes and fittings	20 days	Fri 12-11-21	Wed 01-12-21	126																
128	Hydrotesting	60 days	Thu 02-12-21	Sun 30-01-22	127																
129	Pump House	116 days	Fri 12-11-21	Mon 07-03-22																	
130	columns up to lintel Beams	10 days	Fri 12-11-21	Sun 21-11-21	126																
131	Lintel Beam	12 days	Mon 22-11-21	Fri 03-12-21	130																
132	Columns above lintel beams up to top slab of Pump House	14 days	Sat 04-12-21	Fri 17-12-21	131																
133	Roof structure	20 days	Sat 18-12-21	Thu 06-01-22	132																
134	Brick Work,including plastering inside & outside	30 days	Fri 07-01-22	Sat 05-02-22	133																
135	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Sun 06-02-22	Mon 07-03-22	134																



GAYATRI - RAMKY (P)
 6-3 10th Floor, Sector 14, Gurgaon, Haryana, India. Tel: 012-261-0101
 20114206, Fax: 012-2610415



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
136	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
137	Submission & Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	123																
138	Supply	120 days	Thu 04-11-21	Thu 03-03-22	137FS+90 days																
139	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	133FS+20 days,																
140	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	133FS+20 days,																
141	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	140																
142	Zone_8_CWR-6 of 200 KL Capacity cum Pump Hou	509 days	Thu 25-02-21	Thu 21-07-22																	
143	Handing over of encumbrance Free site by client	1 day	Thu 25-02-21	Thu 25-02-21	5SS+57 days																
144	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
145	Construction of foundation and container wall upto GL	60 days	Wed 04-08-21	Mon 04-10-21	143,144FS+30 days																
146	Super structure container wall	20 days	Tue 05-10-21	Sun 24-10-21	145																
147	Roof structure	30 days	Mon 25-10-21	Tue 23-11-21	146																
148	Pipes and fittings	20 days	Wed 24-11-21	Mon 13-12-21	147																
149	Hydrotesting	60 days	Tue 14-12-21	Fri 11-02-22	148																
150	Pump House	126 days	Wed 24-11-21	Tue 29-03-22																	
151	columns up to lintel Beams	10 days	Wed 24-11-21	Fri 03-12-21	147																
152	Lintel Beam	12 days	Sat 04-12-21	Wed 15-12-21	151																
153	Columns above lintel beams up to top slab of Pump House	14 days	Thu 16-12-21	Wed 29-12-21	152																
154	Roof structure	25 days	Thu 30-12-21	Sun 23-01-22	153																
155	Brick Work,including plastering inside & outsi	35 days	Mon 24-01-22	Sun 27-02-22	154																
156	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Mon 28-02-22	Tue 29-03-22	155																
157	Delivery & Erection of equipments	290 days	Tue 05-10-21	Thu 21-07-22																	
158	Submission & Approval of documents	30 days	Tue 05-10-21	Wed 03-11-21	145																
159	Supply	120 days	Wed 02-02-22	Wed 01-06-22	158FS+90 days																
160	Mechanical Erection	25 days	Thu 02-06-22	Sun 26-06-22	154FS+20 days,																
161	Electrical Works	30 days	Thu 02-06-22	Fri 01-07-22	154FS+20 days,																
162	Instrumentation Works	20 days	Sat 02-07-22	Thu 21-07-22	161																
163	Zone_11_CWR-7 of 100 KL Capacity cum Pump Ho	419 days	Thu 25-02-21	Fri 22-04-22																	
164	Handing over of encumbrance Free site by client	1 day	Thu 25-02-21	Thu 25-02-21	5SS+57 days																
165	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
166	Construction of foundation and container wall upto GL	50 days	Sun 25-07-21	Mon 13-09-21	164,165FS+20 days																
167	Super structure container wall	18 days	Tue 14-09-21	Fri 01-10-21	166																
168	Roof structure	30 days	Sun 03-10-21	Mon 01-11-21	167																
169	Pipes and fittings	20 days	Tue 02-11-21	Sun 21-11-21	168																
170	Hydrotesting	60 days	Mon 22-11-21	Thu 20-01-22	169																
171	Pump House	116 days	Tue 02-11-21	Fri 25-02-22																	



GAYATRI - RAMKY (P)
6-3 10th Floor, Sector 10, Indraprastha Extension, New Delhi - 110028, India
23114296, Fax: 23188435



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
172	columns up to lintel Beams	10 days	Tue 02-11-21	Thu 11-11-21	168																
173	Lintel Beam	12 days	Fri 12-11-21	Tue 23-11-21	172																
174	Columns above lintel beams up to top slab of Pump House	14 days	Wed 24-11-21	Tue 07-12-21	173																
175	Roof structure	20 days	Wed 08-12-21	Mon 27-12-21	174																
176	Brick Work,including plastering inside & outsi	30 days	Tue 28-12-21	Wed 26-01-22	175																
177	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Thu 27-01-22	Fri 25-02-22	176																
178	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
179	Submission& Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	165																
180	Supply	120 days	Thu 04-11-21	Thu 03-03-22	179FS+90 days																
181	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	175FS+20 days,																
182	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	175FS+20 days,																
183	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	182																
184	Zone_14&15_CWR-8 of 100 KL Capacity cum Pump House	428 days	Tue 16-02-21	Fri 22-04-22																	
185	Handing over of encumbrance Free site by client	1 day	Tue 16-02-21	Tue 16-02-21	5SS+48 days																
186	Submission and approval of design & Drawing for CWR, PH	90 days	Mon 05-04-21	Sun 04-07-21	6																
187	Construction of foundation and container wall upto GL	50 days	Wed 04-08-21	Thu 23-09-21	185,186FS+30 days																
188	Super structure container wall	18 days	Fri 24-09-21	Tue 12-10-21	187																
189	Roof structure	30 days	Wed 13-10-21	Thu 11-11-21	188																
190	Pipes and fittings	20 days	Fri 12-11-21	Wed 01-12-21	189																
191	Hydrotesting	60 days	Thu 02-12-21	Sun 30-01-22	190																
192	Pump House	116 days	Fri 12-11-21	Mon 07-03-22																	
193	columns up to lintel Beams	10 days	Fri 12-11-21	Sun 21-11-21	189																
194	Lintel Beam	12 days	Mon 22-11-21	Fri 03-12-21	193																
195	Columns above lintel beams up to top slab of Pump House	14 days	Sat 04-12-21	Fri 17-12-21	194																
196	Roof structure	20 days	Sat 18-12-21	Thu 06-01-22	195																
197	Brick Work,including plastering inside & outsi	30 days	Fri 07-01-22	Sat 05-02-22	196																
198	After completion of rest, works of structure and finishing (Painting, doors, sanitary)	30 days	Sun 06-02-22	Mon 07-03-22	197																
199	Delivery & Erection of equipments	290 days	Mon 05-07-21	Fri 22-04-22																	
200	Submission& Approval of documents	30 days	Mon 05-07-21	Tue 03-08-21	186																
201	Supply	120 days	Thu 04-11-21	Thu 03-03-22	200FS+90 days																
202	Mechanical Erection	25 days	Fri 04-03-22	Mon 28-03-22	196FS+20 days,																
203	Electrical Works	30 days	Fri 04-03-22	Sat 02-04-22	196FS+20 days,																
204	Instrumentation Works	20 days	Sun 03-04-22	Fri 22-04-22	203																
205	Construction of RCC OHT	702 days	Fri 27-11-20	Wed 02-11-22																	
206	Zone_1_OHT-1_600 KL, 18 m staging	624 days	Sun 14-02-21	Wed 02-11-22																	



GAYATRI - RAMKY (P)
6-3 10th Floor, Sector 10, Gurgaon, Haryana, India. Tel: 012-261-0101
2014201, Fax: 012-2610415



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
207	Handing over of encumbrance Free site by client	1 day	Sun 14-02-21	Sun 14-02-21	5SS+46 days															
208	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
209	Construction of foundation columns upto GL	55 days	Tue 20-07-21	Mon 13-09-21	207,208FS+15 c															
210	Columns upto staging including staircase	120 days	Tue 14-09-21	Wed 12-01-22	209															
211	Ring beam/bottom dome/conical dome with balcony	60 days	Thu 13-01-22	Sun 13-03-22	210															
212	Container wall	45 days	Mon 14-03-22	Wed 27-04-22	211															
213	Roof dome	54 days	Thu 28-04-22	Mon 20-06-22	212															
214	Pipes and fittings	30 days	Tue 21-06-22	Wed 20-07-22	213															
215	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Thu 21-07-22	Sat 03-09-22	214															
216	Hydrotesting	60 days	Sun 04-09-22	Wed 02-11-22	215															
217	Zone_2_OHT-2_100 KL, 18 m staging	455 days	Wed 10-02-21	Fri 13-05-22																
218	Handing over of encumbrance Free site by client	1 day	Wed 10-02-21	Wed 10-02-21	5SS+42 days															
219	Submission and approval of design & Drawing for OHT	80 days	Mon 05-04-21	Thu 24-06-21	6															
220	Construction of foundation columns upto GL	41 days	Sun 25-07-21	Sat 04-09-21	218,219FS+30 c															
221	Columns upto staging including staircase	65 days	Sun 05-09-21	Tue 09-11-21	220															
222	Ring beam/bottom dome/conical dome with balcony	30 days	Wed 10-11-21	Thu 09-12-21	221															
223	Container wall	20 days	Fri 10-12-21	Wed 29-12-21	222															
224	Roof dome	25 days	Thu 30-12-21	Sun 23-01-22	223															
225	Pipes and fittings	30 days	Mon 24-01-22	Tue 22-02-22	224															
226	All other finishing works (Grinding,painting,Fixing of lightning arrester	20 days	Wed 23-02-22	Mon 14-03-22	225															
227	Hydrotesting	60 days	Tue 15-03-22	Fri 13-05-22	226															
228	Zone_3_OHT-3_275 KL, 22 m staging	565 days	Sun 14-02-21	Sun 04-09-22																
229	Handing over of encumbrance Free site by client	1 day	Sun 14-02-21	Sun 14-02-21	5SS+46 days															
230	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
231	Construction of foundation columns upto GL	55 days	Sun 25-07-21	Sat 18-09-21	229,230FS+20 c															
232	Columns upto staging including staircase	105 days	Sun 19-09-21	Sun 02-01-22	231															
233	Ring beam/bottom dome/conical dome with balcony	50 days	Mon 03-01-22	Mon 21-02-22	232															
234	Container wall	25 days	Tue 22-02-22	Fri 18-03-22	233															
235	Roof dome	35 days	Sat 19-03-22	Fri 22-04-22	234															
236	Pipes and fittings	30 days	Sat 23-04-22	Sun 22-05-22	235															
237	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Mon 23-05-22	Wed 06-07-22	236															
238	Hydrotesting	60 days	Thu 07-07-22	Sun 04-09-22	237															
239	Zone_4_OHT-4_350 KL, 22 m staging	588 days	Thu 21-01-21	Sun 04-09-22																



GAYATRI - RAMKY (JV)
6-3 10th Floor, Tower, Sankarapada, Ballabgarh Road, Hyderabad - 500 082 Tel: 040
23114256, Fax: 040 - 23188435



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
240	Handing over of encumbrance Free site by client	1 day	Thu 21-01-21	Thu 21-01-21	5SS+23 days															
241	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
242	Construction of foundation columns upto GL	55 days	Tue 20-07-21	Mon 13-09-21	240,241FS+15 c															
243	Columns upto staging including staircase	105 days	Tue 14-09-21	Tue 28-12-21	242															
244	Ring beam/bottom dome/conical dome with balcony	55 days	Wed 29-12-21	Mon 21-02-22	243															
245	Container wall	25 days	Tue 22-02-22	Fri 18-03-22	244															
246	Roof dome	35 days	Sat 19-03-22	Fri 22-04-22	245															
247	Pipes and fittings	30 days	Sat 23-04-22	Sun 22-05-22	246															
248	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Mon 23-05-22	Wed 06-07-22	247															
249	Hydrotesting	60 days	Thu 07-07-22	Sun 04-09-22	248															
250	Zone_5_OHT-5_350 KL, 20 m staging	573 days	Thu 11-02-21	Fri 09-09-22																
251	Handing over of encumbrance Free site by client	1 day	Thu 11-02-21	Thu 11-02-21	5SS+43 days															
252	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
253	Construction of foundation columns upto GL	55 days	Sun 25-07-21	Sat 18-09-21	251,252FS+20 c															
254	Columns upto staging including staircase	105 days	Sun 19-09-21	Sun 02-01-22	253															
255	Ring beam/bottom dome/conical dome with balcony	55 days	Mon 03-01-22	Sat 26-02-22	254															
256	Container wall	25 days	Sun 27-02-22	Wed 23-03-22	255															
257	Roof dome	35 days	Thu 24-03-22	Wed 27-04-22	256															
258	Pipes and fittings	30 days	Thu 28-04-22	Fri 27-05-22	257															
259	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Sat 28-05-22	Mon 11-07-22	258															
260	Hydrotesting	60 days	Tue 12-07-22	Fri 09-09-22	259															
261	Zone_6_OHT-6_300 KL, 20 m staging	581 days	Sat 23-01-21	Tue 30-08-22																
262	Handing over of encumbrance Free site by client	1 day	Sat 23-01-21	Sat 23-01-21	5SS+25 days															
263	Submission and approval of design & Drawing for OHT	85 days	Mon 05-04-21	Tue 29-06-21	6															
264	Construction of foundation columns upto GL	55 days	Tue 20-07-21	Mon 13-09-21	262,263FS+20 c															
265	Columns upto staging including staircase	105 days	Tue 14-09-21	Tue 28-12-21	264															
266	Ring beam/bottom dome/conical dome with balcony	50 days	Wed 29-12-21	Wed 16-02-22	265															
267	Container wall	25 days	Thu 17-02-22	Sun 13-03-22	266															
268	Roof dome	35 days	Mon 14-03-22	Sun 17-04-22	267															
269	Pipes and fittings	30 days	Mon 18-04-22	Tue 17-05-22	268															
270	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Wed 18-05-22	Fri 01-07-22	269															
271	Hydrotesting	60 days	Sat 02-07-22	Tue 30-08-22	270															
272	Zone_7_OHT-7_350 KL, 18 m staging	548 days	Sun 21-02-21	Thu 25-08-22																



GAYATRI - RAMKY (P)
6-3 10th Floor, Tower, Sector 10, Gurgaon, Haryana, India. Phone: 01292 221, 011 23114256, Fax: 011 23114135



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
273	Handing over of encumbrance Free site by client	1 day	Sun 21-02-21	Sun 21-02-21	5SS+53 days															
274	Submission and approval of design & Drawing for OHT	95 days	Mon 05-04-21	Fri 09-07-21	6															
275	Construction of foundation columns upto GL	55 days	Tue 20-07-21	Mon 13-09-21	273,274FS+10 c															
276	Columns upto staging including staircase	95 days	Tue 14-09-21	Sat 18-12-21	275															
277	Ring beam/bottom dome/conical dome with balcony	55 days	Sun 19-12-21	Fri 11-02-22	276															
278	Container wall	25 days	Sat 12-02-22	Tue 08-03-22	277															
279	Roof dome	35 days	Wed 09-03-22	Tue 12-04-22	278															
280	Pipes and fittings	30 days	Wed 13-04-22	Thu 12-05-22	279															
281	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Fri 13-05-22	Sun 26-06-22	280															
282	Hydrotesting	60 days	Mon 27-06-22	Thu 25-08-22	281															
283	Zone_8_OHT-8_200 KL, 16 m staging	504 days	Thu 25-02-21	Sat 16-07-22																
284	Handing over of encumbrance Free site by client	1 day	Thu 25-02-21	Thu 25-02-21	5SS+57 days															
285	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
286	Construction of foundation columns upto GL	45 days	Fri 30-07-21	Mon 13-09-21	284,285FS+25 c															
287	Columns upto staging including staircase	75 days	Tue 14-09-21	Sun 28-11-21	286															
288	Ring beam/bottom dome/conical dome with balcony	45 days	Mon 29-11-21	Wed 12-01-22	287															
289	Container wall	25 days	Thu 13-01-22	Sun 06-02-22	288															
290	Roof dome	30 days	Mon 07-02-22	Tue 08-03-22	289															
291	Pipes and fittings	30 days	Wed 09-03-22	Thu 07-04-22	290															
292	All other finishing works (Grinding,painting,Fixing of lightning arrester	40 days	Fri 08-04-22	Tue 17-05-22	291															
293	Hydrotesting	60 days	Wed 18-05-22	Sat 16-07-22	292															
294	Zone_9_OHT-9_250 KL, 18 m staging	523 days	Tue 16-02-21	Tue 26-07-22																
295	Handing over of encumbrance Free site by client	1 day	Tue 16-02-21	Tue 16-02-21	5SS+48 days															
296	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
297	Construction of foundation columns upto GL	45 days	Sun 25-07-21	Wed 08-09-21	295,296FS+20 c															
298	Columns upto staging including staircase	85 days	Thu 09-09-21	Fri 03-12-21	297															
299	Ring beam/bottom dome/conical dome with balcony	50 days	Sat 04-12-21	Sat 22-01-22	298															
300	Container wall	25 days	Sun 23-01-22	Wed 16-02-22	299															
301	Roof dome	30 days	Thu 17-02-22	Fri 18-03-22	300															
302	Pipes and fittings	30 days	Sat 19-03-22	Sun 17-04-22	301															
303	All other finishing works (Grinding,painting,Fixing of lightning arrester	40 days	Mon 18-04-22	Fri 27-05-22	302															
304	Hydrotesting	60 days	Sat 28-05-22	Tue 26-07-22	303															
305	Zone_10_OHT-10_175 KL, 12 m staging	489 days	Sat 20-02-21	Sun 26-06-22																



GAYATRI - RAMKY (JV)
6-3 10th Floor, Tower, Sankarapada, Bhubaneswar, India-751013
20174256, Fax-0674-2378435



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
306	Handing over of encumbrance Free site by client	1 day	Sat 20-02-21	Sat 20-02-21	5SS+52 days															
307	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
308	Construction of foundation columns upto GL	45 days	Sun 25-07-21	Wed 08-09-21	306,307FS+20 c															
309	Columns upto staging including staircase	60 days	Thu 09-09-21	Mon 08-11-21	308															
310	Ring beam/bottom dome/conical dome with balcony	45 days	Tue 09-11-21	Thu 23-12-21	309															
311	Container wall	25 days	Fri 24-12-21	Mon 17-01-22	310															
312	Roof dome	30 days	Tue 18-01-22	Wed 16-02-22	311															
313	Pipes and fittings	30 days	Thu 17-02-22	Fri 18-03-22	312															
314	All other finishing works (Grinding,painting,Fixing of lightning arrester	40 days	Sat 19-03-22	Wed 27-04-22	313															
315	Hydrotesting	60 days	Thu 28-04-22	Sun 26-06-22	314															
316	Zone_11_OHT-11_250 KL, 14 m staging	494 days	Thu 25-02-21	Wed 06-07-22																
317	Handing over of encumbrance Free site by client	1 day	Thu 25-02-21	Thu 25-02-21	5SS+57 days															
318	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
319	Construction of foundation columns upto GL	45 days	Wed 04-08-21	Sat 18-09-21	317,318FS+30 c															
320	Columns upto staging including staircase	75 days	Sun 19-09-21	Fri 03-12-21	319															
321	Ring beam/bottom dome/conical dome with balcony	50 days	Sat 04-12-21	Sat 22-01-22	320															
322	Container wall	25 days	Sun 23-01-22	Wed 16-02-22	321															
323	Roof dome	30 days	Thu 17-02-22	Fri 18-03-22	322															
324	Pipes and fittings	30 days	Sat 19-03-22	Sun 17-04-22	323															
325	All other finishing works (Grinding,painting,Fixing of lightning arrester	20 days	Mon 18-04-22	Sat 07-05-22	324															
326	Hydrotesting	60 days	Sun 08-05-22	Wed 06-07-22	325															
327	Zone_12_OHT-12_50 KL, 20 m staging	445 days	Wed 03-02-21	Tue 26-04-22																
328	Handing over of encumbrance Free site by client	1 day	Wed 03-02-21	Wed 03-02-21	5SS+35 days															
329	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
330	Construction of foundation columns upto GL	41 days	Sun 25-07-21	Sat 04-09-21	328,329FS+20 c															
331	Columns upto staging including staircase	60 days	Sun 05-09-21	Thu 04-11-21	330															
332	Ring beam/bottom dome/conical dome with balcony	30 days	Fri 05-11-21	Sat 04-12-21	331															
333	Container wall	18 days	Sun 05-12-21	Wed 22-12-21	332															
334	Roof dome	20 days	Thu 23-12-21	Tue 11-01-22	333															
335	Pipes and fittings	25 days	Wed 12-01-22	Sat 05-02-22	334															
336	All other finishing works (Grinding,painting,Fixing of lightning arrester	20 days	Sun 06-02-22	Fri 25-02-22	335															
337	Hydrotesting	60 days	Sat 26-02-22	Tue 26-04-22	336															
338	Zone_14_OHT-14_350 KL, 18 m staging	578 days	Fri 27-11-20	Fri 01-07-22																



GAYATRI - RAMKY (JV)
6-3 10th Floor, Tower, Sector 10, Gurgaon, Haryana, India. Phone: 01292 221000, 01292 221001
2014/2015, Fax: 0129 2210015



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
339	Handing over of encumbrance Free site by client	1 day	Thu 10-06-21	Thu 10-06-21	5SS+161 days															
340	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
341	Construction of foundation columns upto GL	55 days	Sun 25-07-21	Sat 18-09-21	339,340FS+20 c															
342	Columns upto staging including staircase	95 days	Sun 19-09-21	Thu 23-12-21	341															
343	Ring beam/bottom dome/conical dome with balcony	55 days	Fri 24-12-21	Wed 16-02-22	342															
344	Container wall	25 days	Thu 17-02-22	Sun 13-03-22	343															
345	Roof dome	35 days	Mon 14-03-22	Sun 17-04-22	344															
346	Pipes and fittings	30 days	Mon 18-04-22	Tue 17-05-22	345															
347	All other finishing works (Grinding,painting,Fixing of lightning arrester	45 days	Wed 18-05-22	Fri 01-07-22	346															
348	Hydrotesting	60 days	Fri 27-11-20	Mon 25-01-21																
349	Zone_15_OHT-15_200 KL, 20 m staging	480 days	Mon 05-04-21	Sun 31-07-22																
350	Handing over of encumbrance Free site by client	1 day	Thu 01-07-21	Thu 01-07-21	5SS+182 days															
351	Submission and approval of design & Drawing for OHT	90 days	Mon 05-04-21	Sun 04-07-21	6															
352	Construction of foundation columns upto GL	45 days	Mon 09-08-21	Thu 23-09-21	350,351FS+35 c															
353	Columns upto staging including staircase	80 days	Fri 24-09-21	Mon 13-12-21	352															
354	Ring beam/bottom dome/conical dome with balcony	45 days	Tue 14-12-21	Thu 27-01-22	353															
355	Container wall	25 days	Fri 28-01-22	Mon 21-02-22	354															
356	Roof dome	30 days	Tue 22-02-22	Wed 23-03-22	355															
357	Pipes and fittings	30 days	Thu 24-03-22	Fri 22-04-22	356															
358	All other finishing works (Grinding,painting,Fixing of lightning arrester	40 days	Sat 23-04-22	Wed 01-06-22	357															
359	Hydrotesting	60 days	Thu 02-06-22	Sun 31-07-22	358															
360	Pipeline Works	690 days	Sat 19-12-20	Sat 12-11-22																
361	Route selection & finalisation of survey route by Client / PMC	42 days	Sat 19-12-20	Sat 30-01-21	7SS															
362	Submission & Approval of L section, Design	140 days	Wed 10-03-21	Wed 28-07-21	8FS+30 days,36															
363	Supply & Delivery of DI,HDPE & GI pipes	255 days	Mon 19-04-21	Sat 01-01-22	362SS+40 days															
364	Supply & Delivery of Valves including specials	206 days	Fri 09-07-21	Tue 01-02-22	362SS+120 day:															
365	E/W,Laying & Jointing,H.T of Rising main	240 days	Thu 29-07-21	Sun 27-03-22																
366	Intake to WTP	20 days	Thu 29-07-21	Wed 18-08-21	362,363SS+30 c															
367	CWR-1 to OHT-1	60 days	Thu 29-07-21	Mon 27-09-21	362,363SS+40 c															
368	CWR-1 to CWR-2	140 days	Thu 29-07-21	Fri 17-12-21	362,363SS+25 c															
369	CWR-1 to CWR-6	180 days	Thu 29-07-21	Wed 26-01-22	362,363SS+20 c															
370	CWR-2 to CWR-3	80 days	Thu 29-07-21	Mon 18-10-21	362,363SS+40 c															
371	CWR-2 to OHT-6	6 days	Mon 08-11-21	Sat 13-11-21	362,363SS+200															
372	CWR-3 to OHT-2	6 days	Mon 08-11-21	Sat 13-11-21	362,363SS+200															
373	CWR-3 to OHT-3	60 days	Thu 29-07-21	Mon 27-09-21	362,363SS+40 c															



GAYATRI - RAMKY (JV)
 6-3 10th Floor, Sector 10, Connaught Place, New Delhi - 110028, India
 23114256, Fax: 23188435



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	
374	CWR-3 to CWR-4	55 days	Thu 29-07-21	Wed 22-09-21	362,363SS+40 c																
375	CWR-4 to OHT-4	2 days	Mon 08-11-21	Tue 09-11-21	362,363SS+200																
376	CWR-4 to CWR-5	100 days	Thu 29-07-21	Sun 07-11-21	362,363SS+25 c																
377	CWR-5 to OHT-5	6 days	Mon 08-11-21	Sat 13-11-21	362,363SS+200																
378	CWR-5 to OHT-7	80 days	Thu 29-07-21	Mon 18-10-21	362,363SS+40 c																
379	CWR-6 to OHT-8	6 days	Mon 08-11-21	Sat 13-11-21	362,363SS+200																
380	CWR-6 to CWR-7	45 days	Thu 29-07-21	Sun 12-09-21	362,363SS+40 c																
381	CWR-6 to OHT-9	90 days	Thu 29-07-21	Thu 28-10-21	362,363SS+40 c																
382	CWR-6 to OHT-10	110 days	Thu 29-07-21	Wed 17-11-21	362,363SS+25 c																
383	CWR-7 to OHT-11	6 days	Mon 08-11-21	Sat 13-11-21	362,363SS+200																
384	CWR-7 to OHT-12	50 days	Thu 29-07-21	Fri 17-09-21	362,363SS+40 c																
385	CWR-7 to CWR-8	55 days	Thu 29-07-21	Wed 22-09-21	362,363SS+40 c																
386	CWR-8 to OHT-14	65 days	Thu 29-07-21	Sun 03-10-21	362,363SS+40 c																
387	CWR-8 to OHT-15	85 days	Thu 29-07-21	Sat 23-10-21	362,363SS+40 c																
388	Hydrotesting	170 days	Thu 19-08-21	Sat 05-02-22	363SS+120 day																
389	Construction of Valve Chambers	180 days	Tue 28-09-21	Sun 27-03-22	363SS+160 day																
390	Construction of Thrust Blocks/Anchor Blocks	120 days	Mon 08-11-21	Mon 07-03-22	363SS+200 day																
391	E/W,Laying & Jointing,H.T of Distribution main	470 days	Thu 29-07-21	Sat 12-11-22																	
392	Zone_1	400 days	Thu 29-07-21	Sat 03-09-22	362,363SS+90 c																
393	Zone_2	60 days	Thu 19-08-21	Mon 18-10-21	362,363SS+120																
394	Zone_3	200 days	Thu 19-08-21	Mon 07-03-22	362,363SS+120																
395	Zone_4	350 days	Thu 29-07-21	Fri 15-07-22	362,363SS+90 c																
396	Zone_5	350 days	Thu 29-07-21	Fri 15-07-22	362,363SS+90 c																
397	Zone_6	300 days	Thu 29-07-21	Thu 26-05-22	362,363SS+90 c																
398	Zone_7	360 days	Thu 29-07-21	Mon 25-07-22	362,363SS+90 c																
399	Zone_8	180 days	Thu 19-08-21	Tue 15-02-22	362,363SS+120																
400	Zone_9	280 days	Thu 29-07-21	Fri 06-05-22	362,363SS+90 c																
401	Zone_10	270 days	Thu 19-08-21	Mon 16-05-22	362,363SS+120																
402	Zone_11	290 days	Thu 29-07-21	Mon 16-05-22	362,363SS+90 c																
403	Zone_12	60 days	Thu 19-08-21	Mon 18-10-21	362,363SS+120																
404	Zone_14	370 days	Thu 29-07-21	Thu 04-08-22	362,363SS+90 c																
405	Zone_15	180 days	Thu 19-08-21	Tue 15-02-22	362,363SS+120																
406	Hydrotesting	400 days	Sat 18-09-21	Sun 23-10-22	363SS+150 day																
407	Construction of Valve Chambers	360 days	Mon 08-11-21	Wed 02-11-22	363SS+200 day																
408	Construction of Thrust Blocks/Anchor Blocks	320 days	Tue 28-12-21	Sat 12-11-22	363SS+250 day																
409	Construction of Boundrywall at different Locations	360 days	Thu 28-01-21	Tue 25-01-22																	
410	Submission and approval of design & Drawing for Boundry wall	30 days	Thu 28-01-21	Fri 26-02-21	6SS+19 days																
411	Foundation upto plinth beam	250 days	Sat 27-02-21	Sat 06-11-21	410																
412	Brick Work	130 days	Mon 29-03-21	Fri 06-08-21	410FS+30 days																
413	Plastering	240 days	Sat 29-05-21	Tue 25-01-22	410FS+90 days																



Task		External Tasks		Manual Task		Finish-only
Split		External Milestone		Duration-only		Deadline
Milestone		Inactive Task		Manual Summary Rollup		Progress
Summary		Inactive Milestone		Manual Summary		
Project Summary		Inactive Summary		Start-only		

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
414	Fixing of Gate and finishing works	120 days	Tue 07-09-21	Wed 05-01-22	410FS+190 day															
415	Painting	120 days	Sat 28-08-21	Sun 26-12-21	410FS+180 day															
416	Construction of Staff Quarters	433 days	Thu 28-01-21	Fri 08-04-22																
417	Submission and approval of design & Drawing for Staff Quarters	30 days	Thu 28-01-21	Fri 26-02-21	6SS+19 days															
418	Staff Quarters at Intakewell	103 days	Mon 27-12-21	Fri 08-04-22																
419	Foundation upto plinthlevel	20 days	Mon 27-12-21	Sat 15-01-22	417FS+300 day															
420	Super structure & Wall upto Roof slab	14 days	Sun 16-01-22	Sat 29-01-22	419															
421	Roof slab	25 days	Sun 30-01-22	Wed 23-02-22	420															
422	Finishing of civil works	30 days	Thu 24-02-22	Fri 25-03-22	421															
423	Finishing of Electrical installation	14 days	Sat 26-03-22	Fri 08-04-22	422															
424	Staff Quarters at WTP	103 days	Tue 07-12-21	Sat 19-03-22																
425	Foundation upto plinthlevel	20 days	Tue 07-12-21	Sun 26-12-21	417FS+280 day															
426	Super structure & Wall upto Roof slab	14 days	Mon 27-12-21	Sun 09-01-22	425															
427	Roof slab	25 days	Mon 10-01-22	Thu 03-02-22	426															
428	Finishing of civil works	30 days	Fri 04-02-22	Sat 05-03-22	427															
429	Finishing of Electrical installation	14 days	Sun 06-03-22	Sat 19-03-22	428															
430	Staff Quarters at CWR_1	103 days	Thu 28-10-21	Mon 07-02-22																
431	Foundation upto plinthlevel	20 days	Thu 28-10-21	Tue 16-11-21	417FS+240 day															
432	Super structure & Wall upto Roof slab	14 days	Wed 17-11-21	Tue 30-11-21	431															
433	Roof slab	25 days	Wed 01-12-21	Sat 25-12-21	432															
434	Finishing of civil works	30 days	Sun 26-12-21	Mon 24-01-22	433															
435	Finishing of Electrical installation	14 days	Tue 25-01-22	Mon 07-02-22	434															
436	Staff Quarters at CWR_3	103 days	Thu 28-10-21	Mon 07-02-22																
437	Foundation upto plinthlevel	20 days	Thu 28-10-21	Tue 16-11-21	417FS+240 day															
438	Super structure & Wall upto Roof slab	14 days	Wed 17-11-21	Tue 30-11-21	437															
439	Roof slab	25 days	Wed 01-12-21	Sat 25-12-21	438															
440	Finishing of civil works	30 days	Sun 26-12-21	Mon 24-01-22	439															
441	Finishing of Electrical installation	14 days	Tue 25-01-22	Mon 07-02-22	440															
442	Staff Quarters at CWR_4	103 days	Thu 28-10-21	Mon 07-02-22																
443	Foundation upto plinthlevel	20 days	Thu 28-10-21	Tue 16-11-21	417FS+240 day															
444	Super structure & Wall upto Roof slab	14 days	Wed 17-11-21	Tue 30-11-21	443															
445	Roof slab	25 days	Wed 01-12-21	Sat 25-12-21	444															
446	Finishing of civil works	30 days	Sun 26-12-21	Mon 24-01-22	445															
447	Finishing of Electrical installation	14 days	Tue 25-01-22	Mon 07-02-22	446															
448	Staff Quarters at CWR_5	103 days	Wed 17-11-21	Sun 27-02-22																
449	Foundation upto plinthlevel	20 days	Wed 17-11-21	Mon 06-12-21	417FS+260 day															
450	Super structure & Wall upto Roof slab	14 days	Tue 07-12-21	Mon 20-12-21	449															
451	Roof slab	25 days	Tue 21-12-21	Fri 14-01-22	450															
452	Finishing of civil works	30 days	Sat 15-01-22	Sun 13-02-22	451															
453	Finishing of Electrical installation	14 days	Mon 14-02-22	Sun 27-02-22	452															




GAYATRI - RAMKY (P)
6-3 1090, TIB Tower, Sector 14, Gurgaon, Haryana, India. Tel: 012-261-0101
2014201, Fax: 012-2610415



Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

CONSTRUCTION OF JHAKHAUN BIRDHA GROUP OF VILLAGES WATER SUPPLY SCHEME

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter		1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter
						Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan
454	Staff Quarters at CWR_2	103 days	Wed 17-11-21	Sun 27-02-22																
455	Foundation upto plinthlevel	20 days	Wed 17-11-21	Mon 06-12-21	417FS+260 days															
456	Super structure & Wall upto Roof slab	14 days	Tue 07-12-21	Mon 20-12-21	455															
457	Roof slab	25 days	Tue 21-12-21	Fri 14-01-22	456															
458	Finishing of civil works	30 days	Sat 15-01-22	Sun 13-02-22	457															
459	Finishing of Electrical installation	14 days	Mon 14-02-22	Sun 27-02-22	458															
460	Staff Quarters at CWR_6	103 days	Wed 17-11-21	Sun 27-02-22																
461	Foundation upto plinthlevel	20 days	Wed 17-11-21	Mon 06-12-21	417FS+260 days															
462	Super structure & Wall upto Roof slab	14 days	Tue 07-12-21	Mon 20-12-21	461															
463	Roof slab	25 days	Tue 21-12-21	Fri 14-01-22	462															
464	Finishing of civil works	30 days	Sat 15-01-22	Sun 13-02-22	463															
465	Finishing of Electrical installation	14 days	Mon 14-02-22	Sun 27-02-22	464															
466	Staff Quarters at CWR_7	103 days	Wed 17-11-21	Sun 27-02-22																
467	Foundation upto plinthlevel	20 days	Wed 17-11-21	Mon 06-12-21	417FS+260 days															
468	Super structure & Wall upto Roof slab	14 days	Tue 07-12-21	Mon 20-12-21	467															
469	Roof slab	25 days	Tue 21-12-21	Fri 14-01-22	468															
470	Finishing of civil works	30 days	Sat 15-01-22	Sun 13-02-22	469															
471	Finishing of Electrical installation	14 days	Mon 14-02-22	Sun 27-02-22	470															
472	Staff Quarters at CWR_8	103 days	Tue 07-12-21	Sat 19-03-22																
473	Foundation upto plinthlevel	20 days	Tue 07-12-21	Sun 26-12-21	417FS+280 days															
474	Super structure & Wall upto Roof slab	14 days	Mon 27-12-21	Sun 09-01-22	473															
475	Roof slab	25 days	Mon 10-01-22	Thu 03-02-22	474															
476	Finishing of civil works	30 days	Fri 04-02-22	Sat 05-03-22	475															
477	Finishing of Electrical installation	14 days	Sun 06-03-22	Sat 19-03-22	476															
478	House Connections (No's)	330 days	Sat 18-12-21	Sat 12-11-22	406SS+90 days															
479	PTSP(Pillar type stand post) No's	250 days	Wed 16-02-22	Sun 23-10-22	478SS+60 days															
480	Trail Run & Commissioning	90 days	Wed 24-08-22	Mon 21-11-22	17															

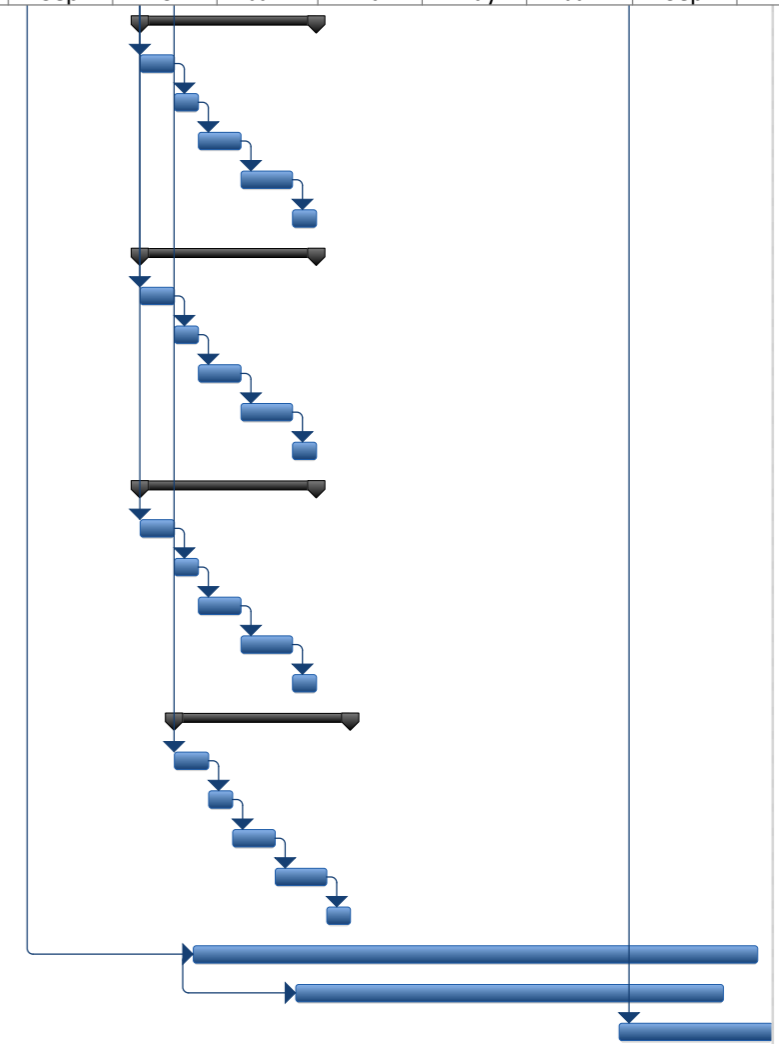

Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			
